

CAMP STANLEY STORAGE ACTIVITY



STORM WATER POLLUTION PREVENTION PLAN TPDES Permit No. TXR150000 RMU-3 Investigation



PARSONS

November 2012

TABLE OF CONTENTS

Owner Name and Address	2
Subcontractor Name and Address.....	2
1.0 PROJECT AND SITE DESCRIPTION.....	2
1.1 Description	2
1.2 Potential Pollutants.....	2
1.3 Schedule	3
1.4 Acres Disturbed.....	3
1.5 Soil Quality	3
1.6 General Location Map.....	4
1.7 Detailed Site Map.....	4
1.8 Support Activities.....	4
1.9 Receiving Water.....	4
1.10 Construction General Permit TX1R50000.....	4
1.11 Notice of Intent.....	5
2.0 BEST MANAGEMENT PRACTICES	5
2.1 Erosion Control and Stabilization Practices.....	5
2.2 Sediment Control Practices	5
2.3 Permanent Storm Water Controls	5
2.4 Applicable State and Local Plans.....	5
2.5 Maintenance Requirements	5
2.6 Inspection of Controls	5

LIST OF FIGURES

Figure 1	CSSA Location Map.....	7
Figure 2	RMU-3 Site Map.....	8
Figure 3	RMU-3 Drainage Control Features.....	9
Figure 4	RMU-1 Firing Range Berm Buildup.....	10

APPENDICES

Appendix A	TCEQ-Construction General Storm Water Permit
Appendix B	Construction Site Notice
Appendix C	Inspection Form

**Storm Water Pollution Prevention Plan
for
RMU-3 Investigations
at
Camp Stanley Storage Activity, Boerne, Texas**

Project Name and Location

Name: Investigation of Contaminated Soils at RMU-3

Location: Bexar County, Texas

Owner Name and Address

Name: Department of the Army

Address: Camp Stanley Storage Activity
25800 Ralph Fair Road
Boerne, TX 78015
Gabriel Moreno-Fergusson
(210) 295-7453

Contractor Name and Address

Name: Parsons Government Services, Inc.

Location: 8000 Centre Park Drive
Suite 200
Austin, Texas 78754
Julie Burdey
(512) 719-6062

Subcontractor Name and Address

Name: USA Environment

Address: 11 Nafta Circle
New Braunfels, Texas 78132
Klay Patteson
(830) 624-8723

1.0 PROJECT AND SITE DESCRIPTION

1.1 DESCRIPTION

The project site is a registered Range Management Unit 3 (RMU-3) located at Camp Stanley Storage Activity (CSSA) (**Figure 1**). The 3.2-acre site is located in the northeastern portion of the Inner Cantonment as shown in **Figure 2** (inset map). It was reportedly used as a rifle range during the 1940s through the 1950s.

1.2 POTENTIAL POLLUTANTS

Based on the historic use of the site, there is potential for metal and explosives concentrations in the surface soils and the firing berm at RMU-3 to be in excess of identified Texas Risk Reduction Program (TRRP) protective concentration limits (PCLs). Also possible are those contaminants typical for excavation equipment, such as hydraulic oil and diesel.

1.3 SCHEDULE

Excavation activities may take place at any time. The investigation is anticipated to take approximately eight weeks. All excavation work will be scheduled in accordance with the operational schedules of nearby CSSA facilities.

Parsons will maintain the following records and will make them readily available upon request:

1. the dates when major grading activities occur;
2. the dates when excavation or sifting activities temporarily or permanently cease on a portion of the site; and
3. the dates when investigation and restoration measures are initiated and completed.

1.4 ACRES DISTURBED

CSSA contains more than 4,000 acres. The area of RMU-3 is 3.2 acre in size. The area of the proposed excavation as shown in **Figure 3** is 1.6 acres. The proposed staging area, approximately 0.44 acres in size, is also as shown on **Figure 3**. Except for the existing dirt road, the surrounding area is vegetated with native grasses, scrubs, and trees. Disturbance of vegetated material outside the proposed excavation and staging area will be limited.

Excavated soil from RMU-3 may be taken to the CSSA East Pasture and used to expand the RMU-1 berm. Soil taken to the RMU-1 berm must contain no large boulders, no munitions and explosives of concern (MEC) items, no metal greater than 6” in diameter, and be non-hazardous (see **Figure 4**).

1.5 SOIL QUALITY

Soils in the vicinity of RMU-3 are classified as Trinity and Frio soils in the west towards Salado Creek, and gently undulating Tarrant association soils in the east of the site by the U.S. Department of Agriculture (USDA) Soil Conservation Service soil survey for Bexar County, Texas (USDA Soil Conservation Service, Bexar County Soil Survey, 1991).

The presence of Trinity and Frio soils in the western half of RMU-3 is due to its proximity to Salado Creek. The Trinity and Frio soils are frequently flooded and are the main channel soils for Salado Creek and its tributaries. The soils occur in narrow, long, and irregularly shaped areas. They are flooded at least once a year after heavy rains. Some areas are subject to thin sediment depositions, while other areas are scoured. Channels are poorly defined and are of small capacity. Trinity soils make up the majority of this soil type and are 3 to 5 feet deep, clayey to gravelly loam. Frio soils are 3 to 4 feet deep, dark grayish-brown clay loam. The soils are generally used as pasture, with occasional cultivation. Additional information about the Trinity and Frio soils can be found in the CSSA Environmental Encyclopedia (Volume 1-1, Background Information Report, Soils and Geology).

Consistent with the topography of RMU-3, the Tarrant soils occur along the outer edges of the Salado Creek floodplain. The soils are shallow and form over hard, fractured limestone. The surface layer is usually about 10 inches thick and consists of a dark grayish-brown, calcareous, clay loam with scattered gravel cobbles, and flagstones. Gently undulating Tarrant Association soils occur as nearly level and gently sloping areas of typical prairie and plateau topography. These soils are best suited for native grasses and range use. Additional information about the Tarrant soils can be found in the CSSA Environmental Encyclopedia (Volume 1-1, Background Information Report, Soils and Geology).

1.6 GENERAL LOCATION MAP

Figure 1 provides the location of the Camp Stanley Storage Activity.

1.7 DETAILED SITE MAPS

Figure 3 show the original site boundary, the proposed excavation extent, the proposed location of the staging area, and Salado Creek located just west of the site.

1.8 SUPPORT ACTIVITIES

All contaminated soils and waste debris will be managed as appropriate in accordance with CSSA's *RFI Interim Measures Waste Management Plan*, Parsons, 2006 and the *RMU-3 RFI/IM Addendum*, November 2012.

Non-hazardous metals-impacted soil may be hauled by truck to the CSSA firing range RMU-1 located in the East Pasture. The soil will be used to build up the existing firing range mound. The addition to the mound will cover less than one acre. Native grass seeds will be planted on the bare soil. A silt fence cannot be erected at this site, since it is an active firing range. The surrounding grass-vegetated area has proven to be sufficient to capture any eroded soil from the mound. See **Figure 4** for a site plan of this area.

1.9 RECEIVING WATER

The elevation of the site ranges from about 1,210 feet above sea level (ASL) on the west side of the site and 1,240 feet ASL on the east side of the site (**Figure 3**). As shown on **Figure 3**, Salado Creek passes from northwest to southeast and is located just west of the site. The site is vegetated by native grasses and a few shrubs.

1.10 CONSTRUCTION GENERAL PERMIT TX1R50000

The March 5, 2008 Construction General Permit TXR150000 is located in **Appendix A**. A copy of the Small Construction Site Notice is located in **Appendix B**. This notice will be displayed at the CSSA bulletin area and within the subcontractor's bulletin area.

1.11 NOTICE OF INTENT

A Notice of Intent is not required for construction sites less than 5 acres.

2.0 BEST MANAGEMENT PRACTICES

The following are the Best Management Practices (BMP) to be utilized at the project site.

2.1 EROSION CONTROL AND STABILIZATION PRACTICES

A silt fence will be placed on the downhill west side of the site, between the excavation and Salado Creek (see **Figure 3**). The excavation area will be stabilized and graded in coordination with CSSA to support the future use of the area. Any disturbed areas, which will not be put to other use, will be seeded with native grass.

Soil identified as containing concentrations of contaminants greater than hazardous toxicity criteria will be stockpiled within the excavated area and covered with plastic. Excavated, non-hazardous soils will remain uncovered. Passenger vehicles and equipment trailers will not enter the excavated area. Excavating equipment will be parked on a trailer prior to leaving CSSA.

2.2 SEDIMENT CONTROL PRACTICES

Sediment will be contained within the excavated and staging area. To retain sediment on-site during storm events, a silt fence will be placed downhill of the excavated area as shown on **Figure 3**.

2.3 PERMANENT STORM WATER CONTROLS

There will be no permanent storm water controls. Site restoration will be coordinated with CSSA, depending on future plans for the area.

2.4 APPLICABLE STATE AND LOCAL PLANS

The Edwards Aquifer Contribution Zone Plan is not applicable to construction sites less than 5 acres.

2.5 MAINTENANCE REQUIREMENTS


When construction activities temporarily or permanently cease, erosion control and stabilization practices will be initiated as required by Section III.F.2(b)(iii) of TPDES Permit No. TXR150000. This includes the initiation of stabilization measures as soon as practicable in portions of the site where construction activities have temporarily ceased and the initiation of measures that provide a protective cover as soon as practicable in portions of the site where construction activities have permanently ceased. As per the TPDES Permit, these measures will be initiated no more than 14 days after the construction activity in that portion of the site has temporarily or permanently ceased.

2.6 INSPECTION OF CONTROLS

All erosion and sediment control measures and other protective measures will be maintained in effective operating condition. Disturbed areas will be inspected once every

14 days to determine if erosion control best management practices (BMPs) are performing appropriately. Inspections will also occur within 24-hours following rainfall events of one-half inch or more. Improperly performing BMPs or control measures will be fixed or replaced, as required, by a more appropriate BMP/control measure as soon as practicable after discovery of any problem. If practicable, maintenance on BMPs that are not operating effectively will be performed before the next anticipated storm event.

Parsons on-site personnel will perform these inspections and complete the inspection form located in **Appendix C**. Kyle Caskey (210) 204-8529, or his designee, of Parsons will review the inspection forms before they are placed in this SWPPP.

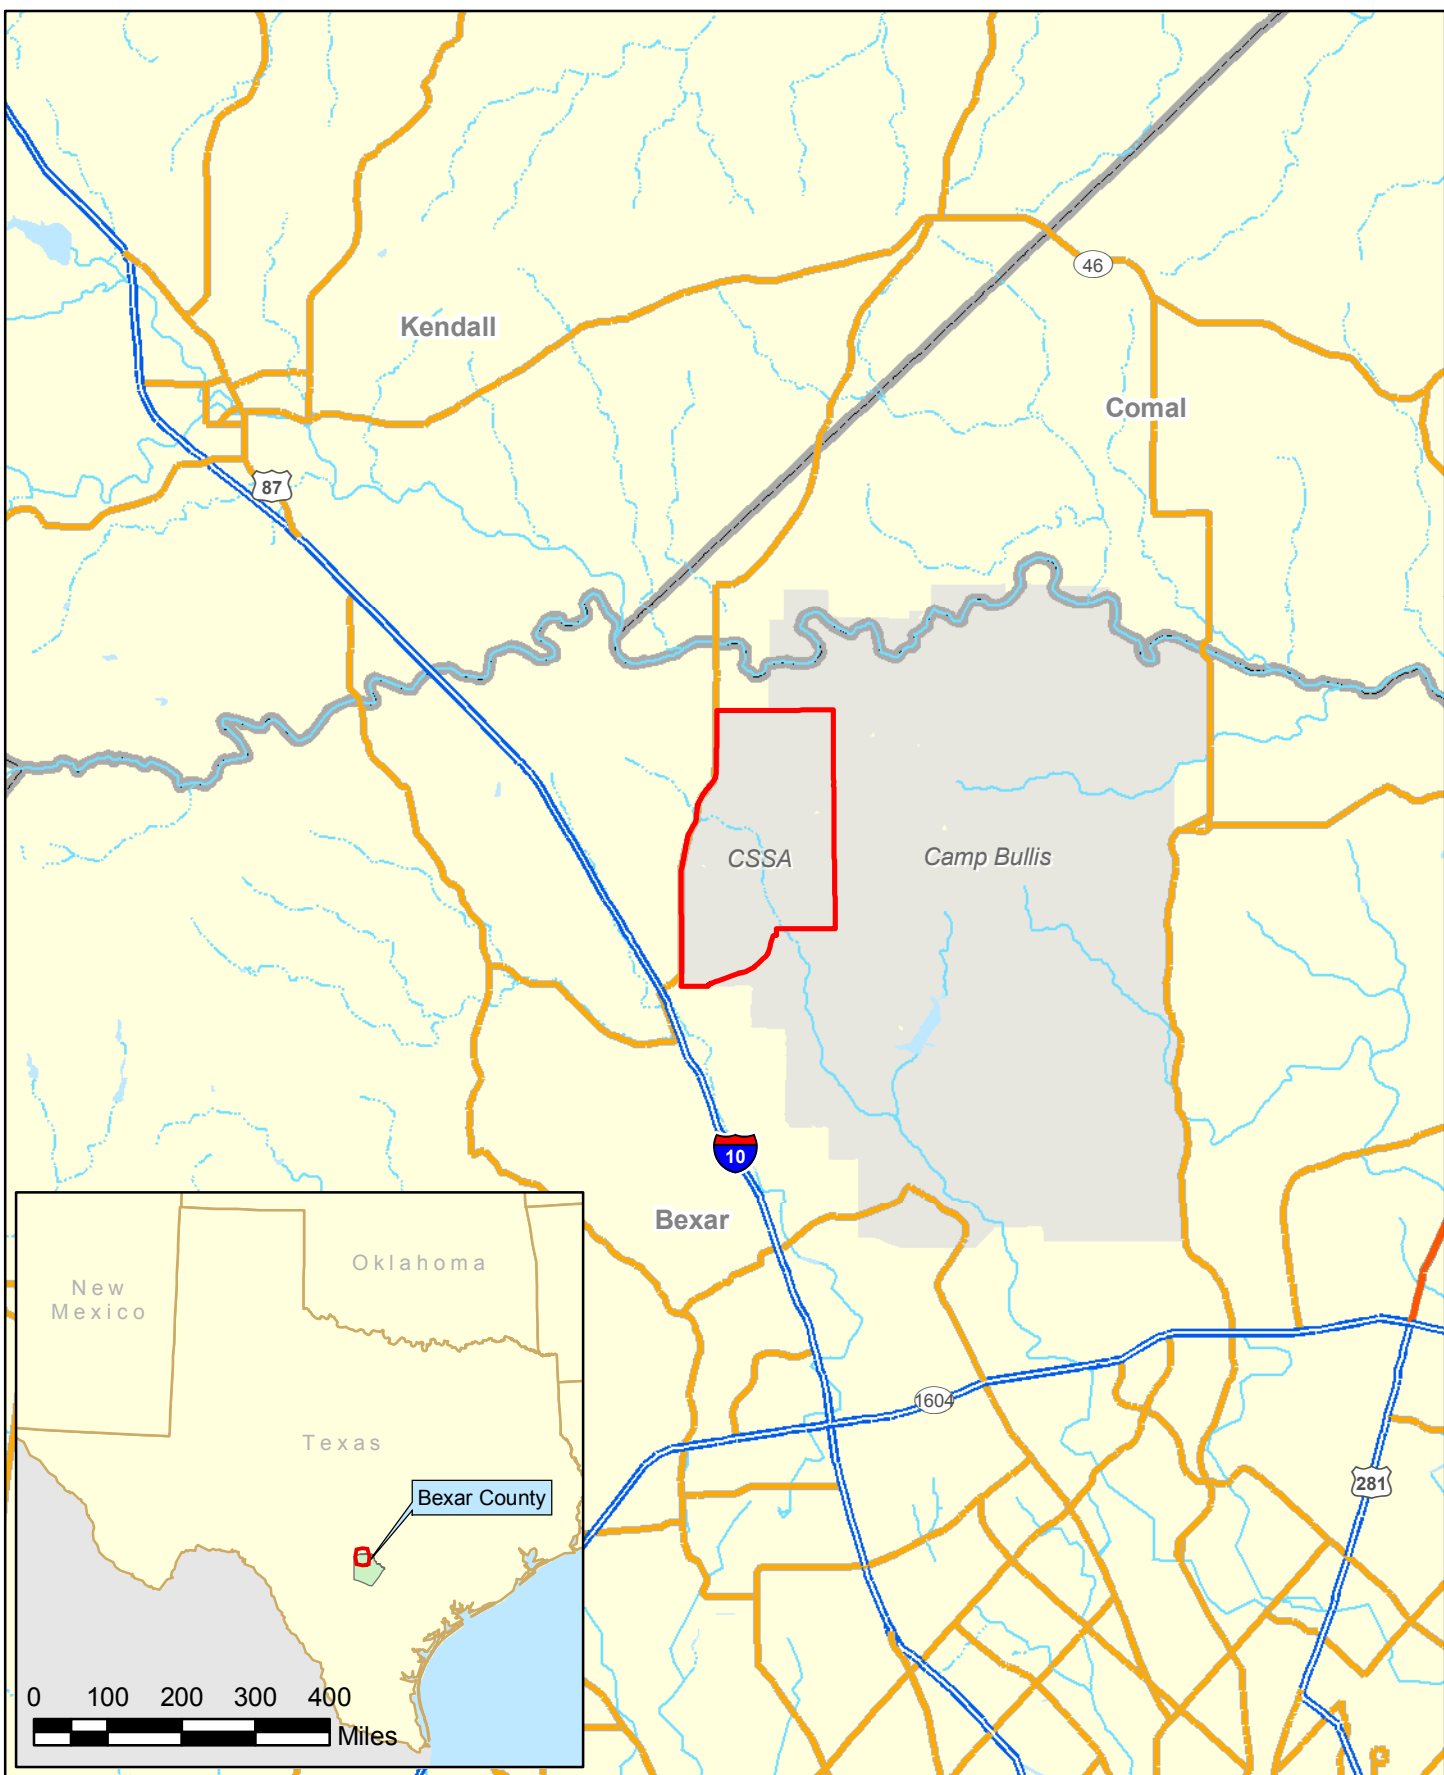

- CSSA
- Freeway
- Highway
- Major Road
- County Boundary
- Military Installation






Figure 1
CSSA Location Map
Camp Stanley Storage Activity

PARSONS



Aerial Photo Date: Jan. 2012



 Intermittent Stream
 Site Boundary


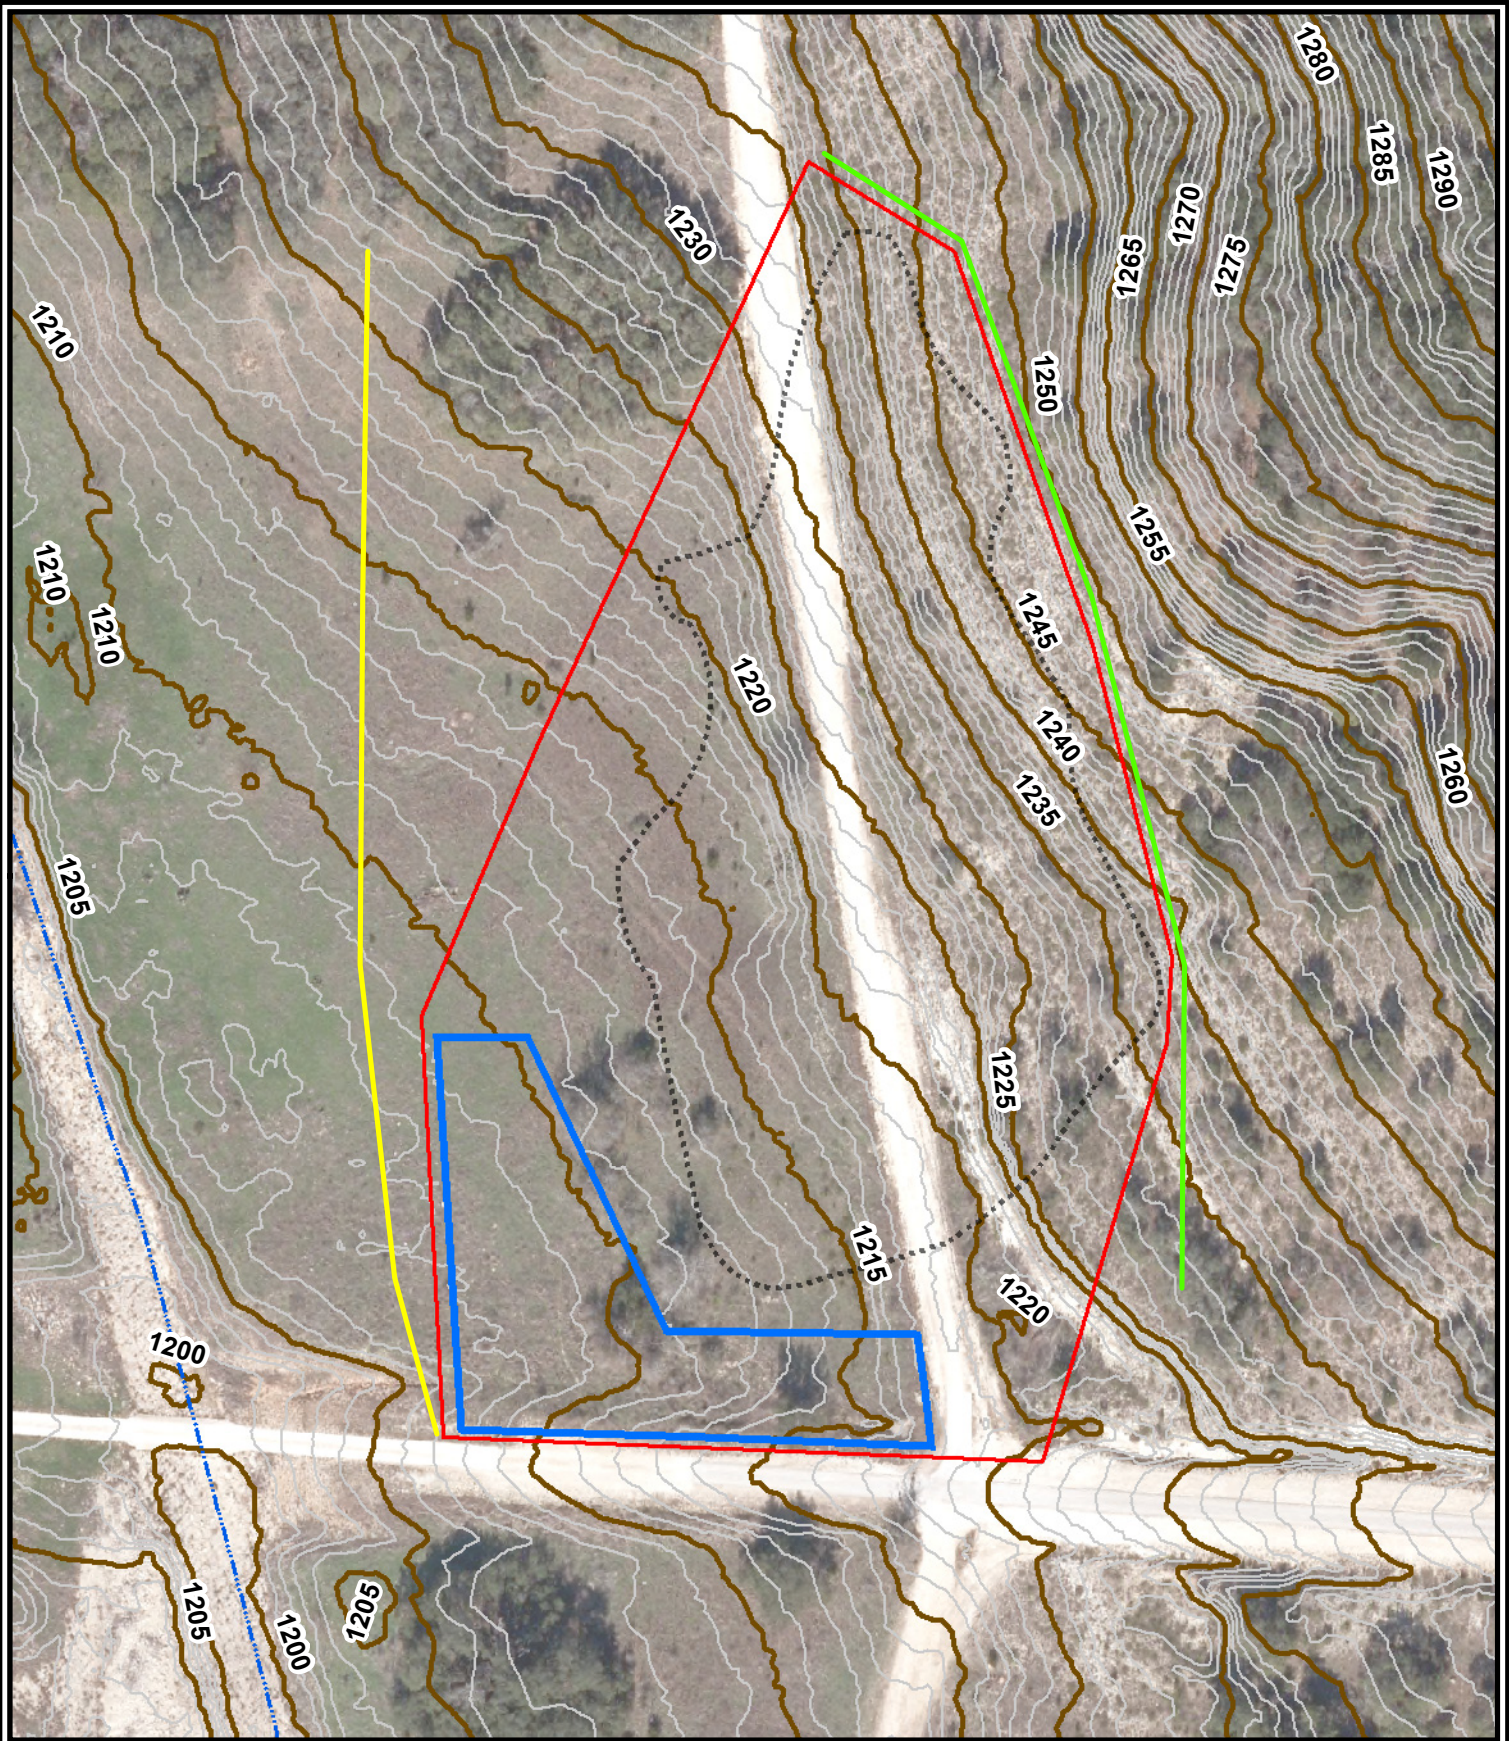
0 25 50 100
 Feet

Figure 2
RMU-3 Site Location Map Camp Stanley Storage Activity
PARSONS




0 25 50 100
 Feet

- Proposed Silt Fence
- Proposed Diversion Berm
- Proposed Excavation Extent
- Proposed Staging Area
- - - Intermittent Stream
- 5 Foot Contours
- 1 Foot Contours
- RMU-3 Boundary

Figure 3

RMU-3
 Drainage Control Features
 Camp Stanley Storage Activity

PARSONS

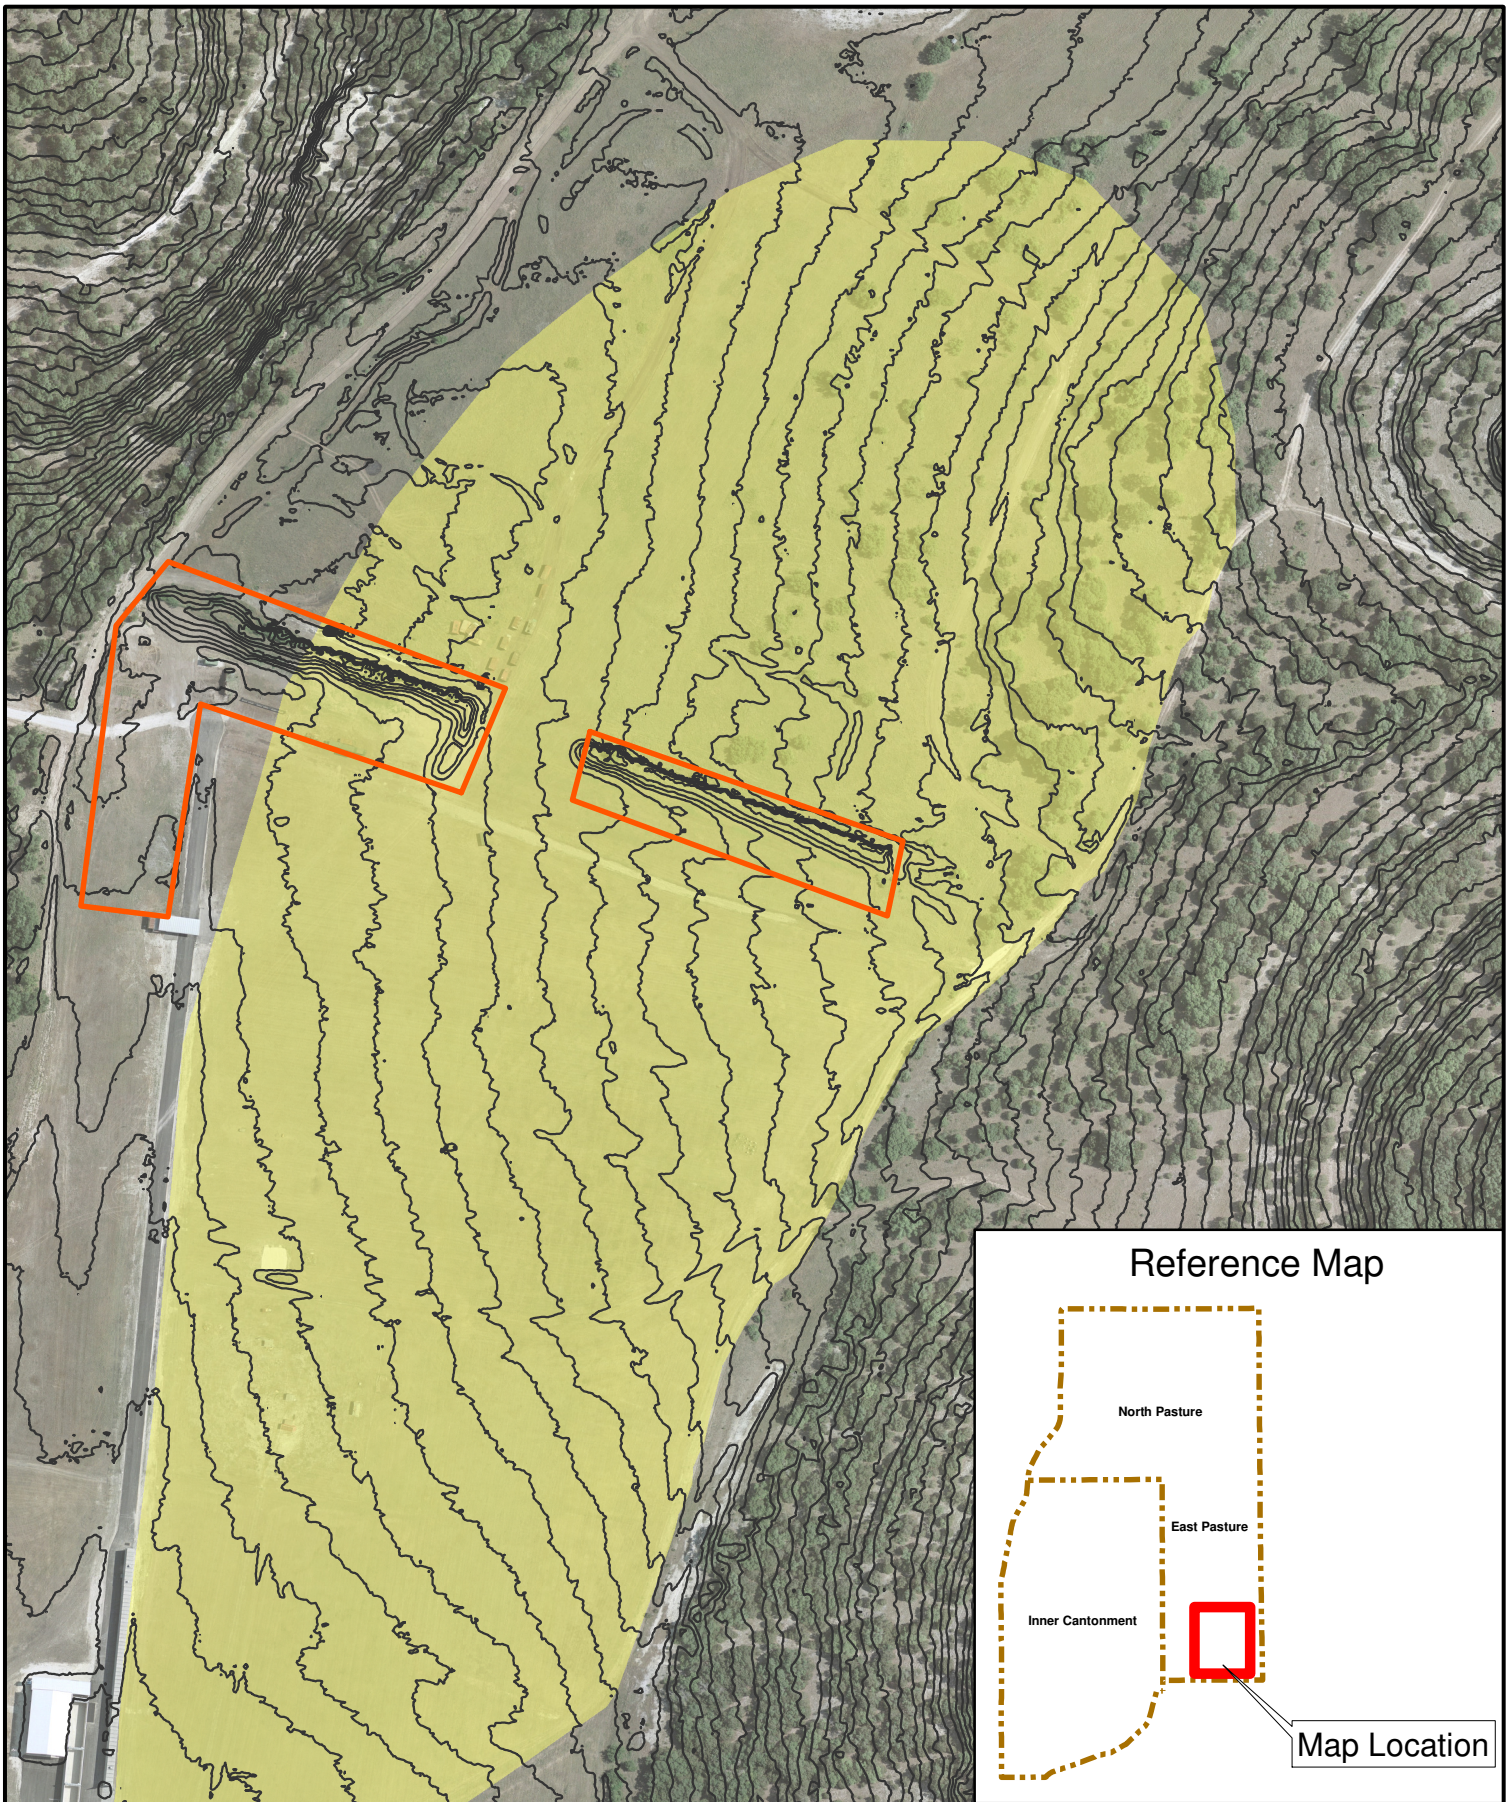

0 300 600 Feet

- Berm Buildup Area
- RMU-1
- 2 ft Elevation Contours

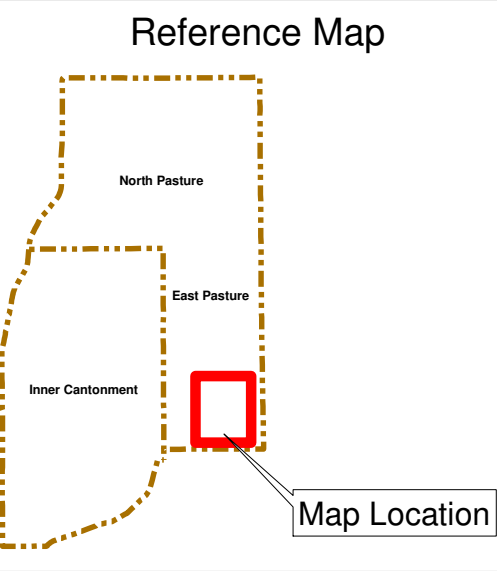


Figure 4
 RMU-1 Firing Range Berm Buildup
 Camp Stanley Storage Activity

PARSONS

APPENDIX A
TCEQ – CONSTRUCTION GENERAL STORM WATER PERMIT



TCEQ Docket No. 2007-1588-WQ
TPDES General Permit No. TXR150000

**TEXAS COMMISSION ON ENVIRONMENTAL
QUALITY**
P.O. BOX 13087
Austin, TX 78711-3087

This is a renewal of TPDES
General Permit No. TXR150000,
issued March 5, 2003.

GENERAL PERMIT TO DISCHARGE WASTES

under provisions of
Section 402 of the Clean Water Act
and Chapter 26 of the Texas Water Code

Construction sites that discharge storm water associated with construction activity

located in the state of Texas

may discharge to surface water in the state

only according to effluent limitations, monitoring requirements and other conditions set forth in this permit, as well as the rules of the Texas Commission on Environmental Quality (TCEQ), the laws of the State of Texas, and other orders of the TCEQ. The issuance of this general permit does not grant to the permittee the right to use private or public property for conveyance of storm water and certain non-storm water discharges along the discharge route. This includes property belonging to but not limited to any individual, partnership, corporation or other entity. Neither does this permit authorize any invasion of personal rights nor any violation of federal, state, or local laws or regulations. It is the responsibility of the permittee to acquire property rights as may be necessary to use the discharge route.

This permit and the authorization contained herein shall expire at midnight on March 5, 2013.

EFFECTIVE DATE: March 5, 2008

ISSUED DATE: **FEB 15 2008**

Buddy Corcix

For the Commission

TPDES GENERAL PERMIT NUMBER TXR150000 RELATING TO STORM WATER DISCHARGES ASSOCIATED WITH CONSTRUCTION ACTIVITIES

Table of Contents

Part I. Flow Chart and Definitions.....Page 3

Part II. Permit Applicability and Coverage.....Page 10

Part III. Storm Water Pollution Prevention PlansPage 25

Part IV. Storm Water Runoff from Concrete Batch PlantsPage 37

Part V. Concrete Truck Wash Out RequirementsPage 42

Part VI. Retention of RecordsPage 42

Part VII. Standard Permit ConditionsPage 43

Part VIII. FeesPage 44

Appendix A. Automatic Authorization - Periods of Low Erosion Potential by CountyPage 45

Appendix B. Erosivity Index (EI) Zones in Texas.....Page 46

Appendix C. Isoerodent MapPage 47

Appendix D. Erosivity Indices for EI Zones in TexasPage 48

Attachment 1. Small Construction Site Notice: Low Potential for Erosion.....Page 49


Attachment 2. Small Construction Site Notice.....Page 50

Attachment 3. Large Construction Site Notice: "Secondary Operator" NoticePage 51

Attachment 4. Large Construction Site Notice: "Primary Operator" NoticePage 52

Part I. Flow Chart and Definitions

Section A. Flow Chart to Determine Whether Coverage is Required

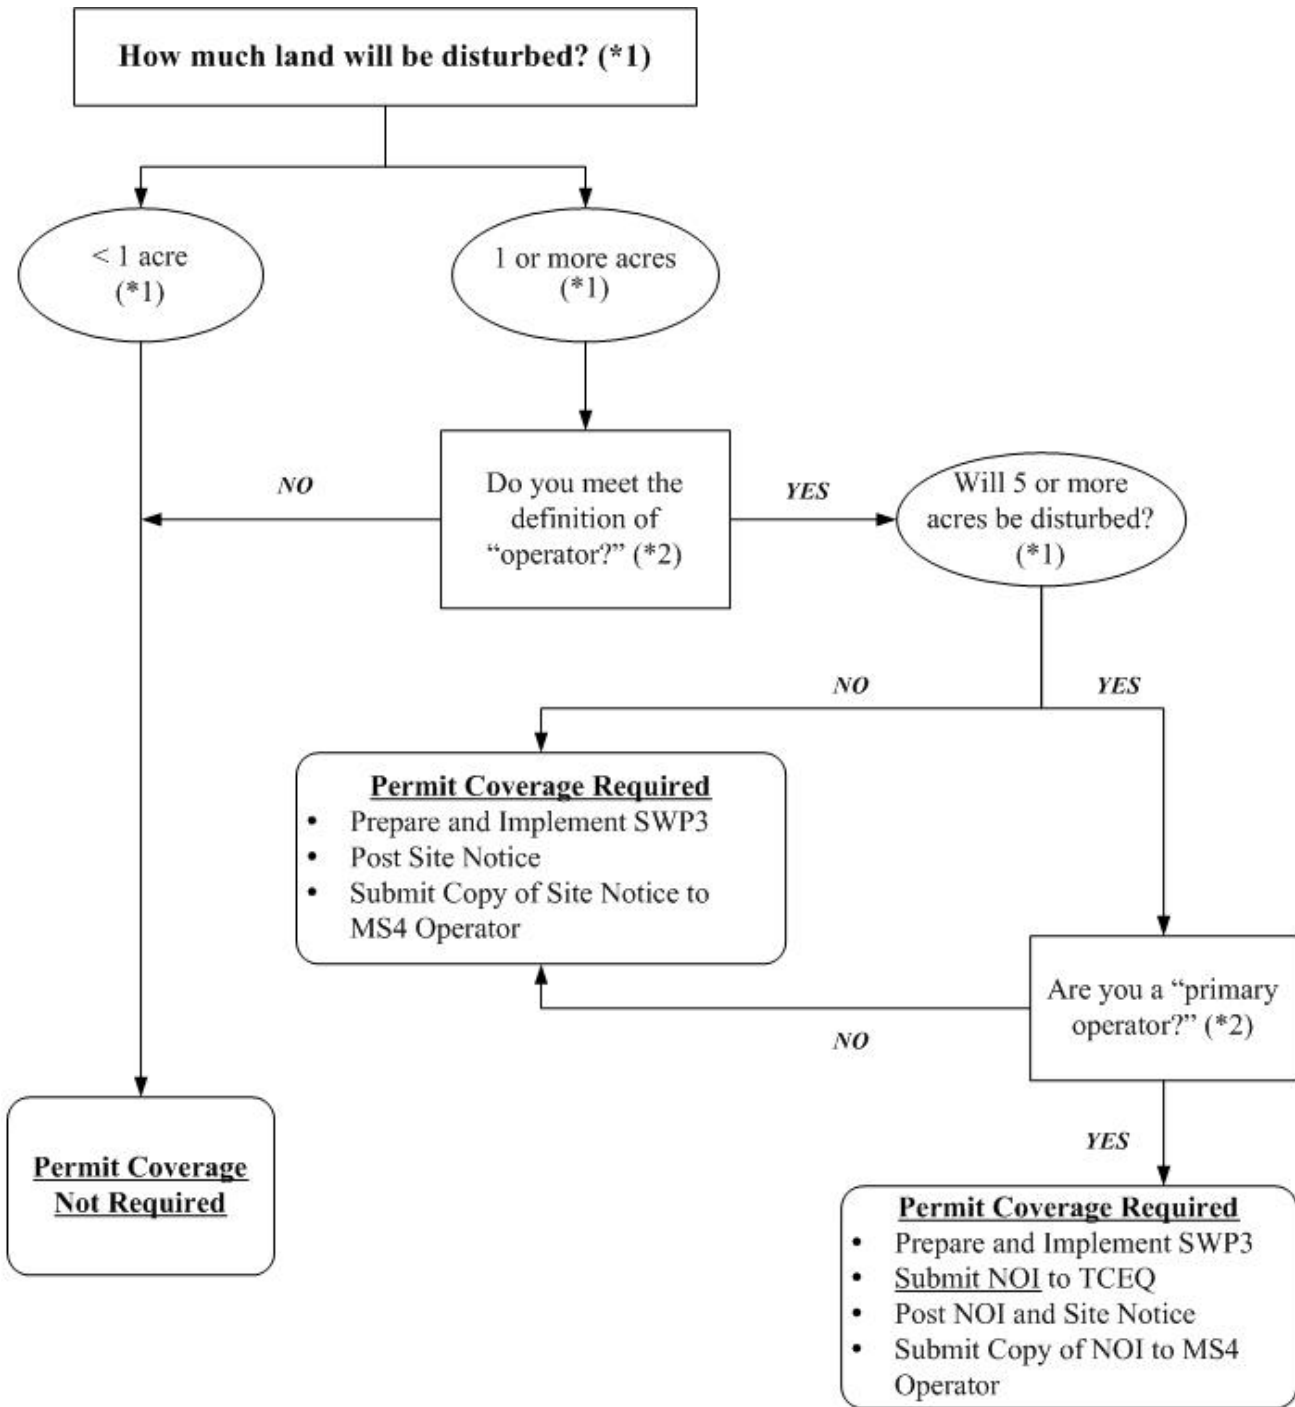

(*1) To determine the size of the construction project, use the size of the entire area to be disturbed, and include the size of the larger common plan of development or sale, if the project is part of a larger project (refer to Part I.B., "Definitions," for an explanation of "larger common plan of development or sale").

(*2) Refer to the definitions for "operator," "primary operator," and "secondary operator" in Part I., Section B. of this permit.

Section B. Definitions

Arid Areas - Areas with an average annual rainfall of 0 to 10 inches.

Best Management Practices (BMPs) - Schedules of activities, prohibitions of practices, maintenance procedures, structural controls, local ordinances, and other management practices to prevent or reduce the discharge of pollutants. BMPs also include treatment requirements, operating procedures, and practices to control construction site runoff, spills or leaks, waste disposal, or drainage from raw material storage areas.

Commencement of Construction - The initial disturbance of soils associated with clearing, grading, or excavation activities, as well as other construction-related activities (e.g., stockpiling of fill material, demolition)

Common Plan of Development - A construction activity that is completed in separate stages, separate phases, or in combination with other construction activities. A common plan of development (also known as a “common plan of development or sale”) is identified by the documentation for the construction project that identifies the scope of the project, and may include plats, blueprints, marketing plans, contracts, building permits, a public notice or hearing, zoning requests, or other similar documentation and activities. A common plan of development does not necessarily include all construction projects within the jurisdiction of a public entity (e.g., a city or university). Construction of roads or buildings in different parts of the jurisdiction would be considered separate “common plans,” with only the interconnected parts of a project being considered part of a “common plan” (e.g., a building and its associated parking lot and driveways, airport runway and associated taxiways, a building complex, etc.). Where discrete construction projects occur within a larger common plan of development or sale but are located ¼ mile or more apart, and the area between the projects is not being disturbed, each individual project can be treated as a separate plan of development or sale, provided that any interconnecting road, pipeline or utility project that is part of the same “common plan” is not included in the area to be disturbed.

Discharge – For the purposes of this permit, the drainage, release, or disposal of pollutants in storm water and certain non-storm water from areas where soil disturbing activities (e.g., clearing, grading, excavation, stockpiling of fill material, and demolition), construction materials or equipment storage or maintenance (e.g., fill piles, borrow area, concrete truck washout, fueling), or other industrial storm water directly related to the construction process (e.g., concrete or asphalt batch plants) are located.

Edwards Aquifer - As defined under Texas Administrative Code § 213.3 of this title (relating to the Edwards Aquifer), that portion of an arcuate belt of porous, water-bearing, predominantly carbonate rocks known as the Edwards and Associated Limestones in the Balcones Fault Zone trending from west to east to northeast in Kinney, Uvalde, Medina, Bexar, Comal, Hays, Travis, and Williamson Counties; and composed of the Salmon Peak Limestone, McKnight Formation, West Nueces Formation, Devil’s River Limestone, Person Formation, Kainer Formation, Edwards Formation, and Georgetown Formation. The permeable aquifer units generally overlie the less-permeable Glen Rose Formation to the south, overlie the less-permeable Comanche Peak and Walnut Formations north of the Colorado River, and underlie the less-permeable Del Rio Clay regionally.

Edwards Aquifer Recharge Zone - Generally, that area where the stratigraphic units constituting the Edwards Aquifer crop out, including the outcrops of other geologic formations in proximity to the Edwards Aquifer, where caves, sinkholes, faults, fractures, or other permeable features would create a potential for recharge of surface waters into the Edwards Aquifer. The recharge zone is identified as that area designated as such on official maps located in the offices of the Texas Commission on Environmental Quality and the

appropriate regional office. The Edwards Aquifer Map Viewer, located at http://www.tceq.state.tx.us/compliance/field_ops/eapp/mapdisclaimer.html, can be used to determine where the recharge zone is located.

Edwards Aquifer Contributing Zone - The area or watershed where runoff from precipitation flows downgradient to the recharge zone of the Edwards Aquifer. The contributing zone is located upstream (upgradient) and generally north and northwest of the recharge zone for the following counties: all areas within Kinney County, except the area within the watershed draining to Segment 2304 of the Rio Grande Basin; all areas within Uvalde, Medina, Bexar, and Comal Counties; all areas within Hays and Travis Counties, except the area within the watersheds draining to the Colorado River above a point 1.3 miles upstream from Tom Miller Dam, Lake Austin at the confluence of Barrow Brook Cove, Segment 1403 of the Colorado River Basin; and all areas within Williamson County, except the area within the watersheds draining to the Lampasas River above the dam at Stillhouse Hollow reservoir, Segment 1216 of the Brazos River Basin. The contributing zone is illustrated on the Edwards Aquifer map viewer at http://www.tceq.state.tx.us/compliance/field_ops/eapp/mapdisclaimer.html.

Facility or Activity – For the purpose of this permit, a construction site or construction support activity that is regulated under this general permit, including all contiguous land and fixtures (e.g., ponds and materials stockpiles), structures, or appurtenances used at a construction site or industrial site described by this general permit.

Final Stabilization - A construction site status where any of the following conditions are met:

- (a) All soil disturbing activities at the site have been completed and a uniform (i.e., evenly distributed, without large bare areas) perennial vegetative cover with a density of at least 70% of the native background vegetative cover for the area has been established on all unpaved areas and areas not covered by permanent structures, or equivalent permanent stabilization measures (such as the use of riprap, gabions, or geotextiles) have been employed.
- (b) For individual lots in a residential construction site by either:
 - (1) the homebuilder completing final stabilization as specified in condition (a) above; or
 - (2) the homebuilder establishing temporary stabilization for an individual lot prior to the time of transfer of the ownership of the home to the buyer and after informing the homeowner of the need for, and benefits of, final stabilization. If temporary stabilization is not feasible, then the homebuilder may fulfill this requirement by retaining perimeter controls or other best management practices, and informing the homeowner of the need for removal of temporary controls and the establishment of final stabilization.
- (c) For construction activities on land used for agricultural purposes (e.g. pipelines across crop or range land), final stabilization may be accomplished by returning the disturbed land to its preconstruction agricultural use. Areas disturbed that were not previously used for agricultural activities, such as buffer strips immediately adjacent to surface water and areas that are not being returned to their preconstruction agricultural use must meet the final stabilization conditions of condition (a) above.

- (d) In arid, semi-arid, and drought-stricken areas only, all soil disturbing activities at the site have been completed and both of the following criteria have been met:
- (1) Temporary erosion control measures (e.g., degradable rolled erosion control product) are selected, designed, and installed along with an appropriate seed base to provide erosion control for at least three years without active maintenance by the operator, and
 - (2) The temporary erosion control measures are selected, designed, and installed to achieve 70 percent vegetative coverage within three years.

Hyperchlorination of Waterlines – Treatment of potable water lines or tanks with chlorine for disinfection purposes, typically following repair or partial replacement of the waterline or tank, and subsequently flushing the contents.

Indian Country Land – (from 40 CFR 122.2) (1) all land within the limits of any Indian reservation under the jurisdiction of the United States government, notwithstanding the issuance of any patent, and, including rights-of-way running through the reservation; (2) all dependent Indian communities with the borders of the United States whether within the originally or subsequently acquired territory thereof, and whether within or without the limits of a state; and (3) all Indian allotments, the Indian titles to which have not been extinguished, including rights-of-way running through the same.

Indian Tribe - (from 40 CFR 122.2) any Indian Tribe, band, group, or community recognized by the Secretary of the Interior and exercising governmental authority over a Federal Indian Reservation.

Large Construction Activity - Construction activities including clearing, grading, and excavating that result in land disturbance of equal to or greater than five (5) acres of land. Large construction activity also includes the disturbance of less than five (5) acres of total land area that is part of a larger common plan of development or sale if the larger common plan will ultimately disturb equal to or greater than five (5) acres of land. Large construction activity does not include routine maintenance that is performed to maintain the original line and grade, hydraulic capacity, or original purpose of the site (e.g., the routine grading of existing dirt roads, asphalt overlays of existing roads, the routine clearing of existing right-of-ways, and similar maintenance activities.)

Municipal Separate Storm Sewer System (MS4) - A separate storm sewer system owned or operated by the United States, a state, city, town, county, district, association, or other public body (created by or pursuant to state law) having jurisdiction over the disposal of sewage, industrial wastes, storm water, or other wastes, including special districts under state law such as a sewer district, flood control or drainage district, or similar entity, or an Indian tribe or an authorized Indian tribal organization, that discharges to surface water in the state.

Notice of Change (NOC) – Written notification to the executive director from a discharger authorized under this permit, providing changes to information that was previously provided to the agency in a notice of intent form.

Notice of Intent (NOI) - A written submission to the executive director from an applicant requesting coverage under this general permit.

Notice of Termination (NOT) - A written submission to the executive director from a discharger authorized under a general permit requesting termination of coverage.

Operator - The person or persons associated with a large or small construction activity that is either a primary or secondary operator as defined below:

Primary Operator – the person or persons associated with a large or small construction activity that meets either of the following two criteria:

- (a) the person or persons have operational control over construction plans and specifications, including the ability to make modifications to those plans and specifications; or
- (b) the person or persons have day-to-day operational control of those activities at a construction site that are necessary to ensure compliance with a storm water pollution prevention plan (SWP3) for the site or other permit conditions (e.g., they are authorized to direct workers at a site to carry out activities required by the SWP3 or comply with other permit conditions).

Secondary Operator – The person whose operational control is limited to the employment of other operators or to the ability to approve or disapprove changes to plans and specifications. A secondary operator is also defined as a primary operator and must comply with the permit requirements for primary operators if there are no other operators at the construction site.

Outfall - For the purpose of this permit, a point source at the point where storm water runoff associated with construction activity discharges to surface water in the state and does not include open conveyances connecting two municipal separate storm sewers, or pipes, tunnels, or other conveyances that connect segments of the same stream or other water of the U.S. and are used to convey waters of the U.S.

Permittee - An operator authorized under this general permit. The authorization may be gained through submission of a notice of intent, by waiver, or by meeting the requirements for automatic coverage to discharge storm water runoff and certain non-storm water discharges.

Point Source – (from 40 CFR §122.2) Any discernible, confined, and discrete conveyance, including but not limited to, any pipe, ditch, channel, tunnel, conduit, well, discrete fissure, container, rolling stock concentrated animal feeding operation, landfill leachate collection system, vessel or other floating craft from which pollutants are, or may be, discharged. This term does not include return flows from irrigated agriculture or agricultural storm water runoff.

Pollutant - Dredged spoil, solid waste, incinerator residue, sewage, garbage, sewage sludge, filter backwash, munitions, chemical wastes, biological materials, radioactive materials, heat, wrecked or discarded equipment, rock, sand, cellar dirt, and industrial, municipal, and agricultural waste discharged into any surface water in the state. The term "pollutant" does not include tail water or runoff water from irrigation or rainwater runoff from cultivated or uncultivated rangeland, pastureland, and farmland. For the purpose of this permit, the term "pollutant" includes sediment.

Pollution - (from Texas Water Code §26.001(14)) The alteration of the physical, thermal, chemical, or biological quality of, or the contamination of, any surface water in the state that renders the water harmful, detrimental, or injurious to humans, animal life, vegetation, or property or to public health, safety, or welfare, or impairs the usefulness or the public enjoyment of the water for any lawful or reasonable purpose.

Rainfall Erosivity Factor (R factor) - the total annual erosive potential that is due to climatic effects, and is part of the Revised Universal Soil Loss Equation (RUSLE).

Semiarid Areas - areas with an average annual rainfall of 10 to 20 inches

Separate Storm Sewer System - A conveyance or system of conveyances (including roads with drainage systems, streets, catch basins, curbs, gutters, ditches, man-made channels, or storm drains), designed or used for collecting or conveying storm water; that is not a combined sewer, and that is not part of a publicly owned treatment works (POTW).

Small Construction Activity - Construction activities including clearing, grading, and excavating that result in land disturbance of equal to or greater than one (1) acre and less than five (5) acres of land. Small construction activity also includes the disturbance of less than one (1) acre of total land area that is part of a larger common plan of development or sale if the larger common plan will ultimately disturb equal to or greater than one (1) and less than five (5) acres of land. Small construction activity does not include routine maintenance that is performed to maintain the original line and grade, hydraulic capacity, or original purpose of the site (e.g., the routine grading of existing dirt roads, asphalt overlays of existing roads, the routine clearing of existing right-of-ways, and similar maintenance activities.)

Storm Water (or Storm Water Runoff) - Rainfall runoff, snow melt runoff, and surface runoff and drainage.

Storm Water Associated with Construction Activity - Storm water runoff from a construction activity where soil disturbing activities (including clearing, grading, excavating) result in the disturbance of one (1) or more acres of total land area, or are part of a larger common plan of development or sale that will result in disturbance of one (1) or more acres of total land area.

Structural Control (or Practice) - A pollution prevention practice that requires the construction of a device, or the use of a device, to capture or prevent pollution in storm water runoff. Structural controls and practices may include but are not limited to: silt fences, earthen dikes, drainage swales, sediment traps, check dams, subsurface drains, storm drain inlet protection, rock outlet protection, reinforced soil retaining systems, gabions, and temporary or permanent sediment basins.

Surface Water in the State - Lakes, bays, ponds, impounding reservoirs, springs, rivers, streams, creeks, estuaries, wetlands, marshes, inlets, canals, the Gulf of Mexico inside the territorial limits of the state (from the mean high water mark (MHW) out 10.36 miles into the Gulf), and all other bodies of surface water, natural or artificial, inland or coastal, fresh or salt, navigable or nonnavigable, and including the beds and banks of all water-courses and bodies of surface water, that are wholly or partially inside or bordering the state or subject to the jurisdiction of the state; except that waters in treatment systems which are authorized by state or federal law, regulation, or permit, and which are created for the purpose of waste treatment are not considered to be water in the state.

Temporary Stabilization - A condition where exposed soils or disturbed areas are provided a protective cover or other structural control to prevent the migration of pollutants. Temporary stabilization may include temporary seeding, geotextiles, mulches, and other techniques to reduce or eliminate erosion until either permanent stabilization can be achieved or until further construction activities take place.

Waters of the United States - (from 40 CFR, Part 122, Section 2) Waters of the United States or waters of the U.S. means:

- (a) all waters which are currently used, were used in the past, or may be susceptible to use in interstate or foreign commerce, including all waters which are subject to the ebb and flow of the tide;
- (b) all interstate waters, including interstate wetlands;
- (c) all other waters such as intrastate lakes, rivers, streams (including intermittent streams), mudflats, sandflats, wetlands, sloughs, prairie potholes, wet meadows, playa lakes, or natural ponds that the use, degradation, or destruction of which would affect or could affect interstate or foreign commerce including any such waters:
 - (1) which are or could be used by interstate or foreign travelers for recreational or other purposes;
 - (2) from which fish or shellfish are or could be taken and sold in interstate or foreign commerce; or
 - (3) which are used or could be used for industrial purposes by industries in interstate commerce;
- (d) all impoundments of waters otherwise defined as waters of the United States under this definition;
- (e) tributaries of waters identified in paragraphs (a) through (d) of this definition;
- (f) the territorial sea; and
- (g) wetlands adjacent to waters (other than waters that are themselves wetlands) identified in paragraphs (a) through (f) of this definition.

Waste treatment systems, including treatment ponds or lagoons designed to meet the requirements of CWA (other than cooling ponds as defined in 40 CFR §423.11(m) which also meet the criteria of this definition) are not waters of the United States. This exclusion applies only to manmade bodies of water which neither were originally created in waters of the United States (such as disposal area in wetlands) nor resulted from the impoundment of waters of the United States. Waters of the United States do not include prior converted cropland. Notwithstanding the determination of an area's status as prior converted cropland by any other federal agency, for the purposes of the Clean Water Act, the final authority regarding Clean Water Act jurisdiction remains with EPA.

Part II. Permit Applicability and Coverage

Section A. Discharges Eligible for Authorization

1. Storm Water Associated with Construction Activity

Discharges of storm water runoff from small and large construction activities may be authorized under this general permit.

2. Discharges of Storm Water Associated with Construction Support Activities

Examples of construction support activities include, but are not limited to, concrete batch plants, rock crushers, asphalt batch plants, equipment staging areas, material storage yards, material borrow areas, and excavated material disposal areas. Discharges of storm water runoff from construction support activities may be authorized under this general permit, provided that the following conditions are met:

- (a) the activities are located within one (1)-mile from the boundary of the permitted construction site and directly support the construction activity;
- (b) a storm water pollution prevention plan is developed according to the provisions of this general permit and includes appropriate controls and measures to reduce erosion and discharge of pollutants in storm water runoff from the construction support activities; and
- (c) the construction support activities either do not operate beyond the completion date of the construction activity or are authorized under separate TPDES authorization. Separate TPDES authorization may include the TPDES Multi Sector General Permit, TXR050000 (related to storm water discharges associated with industrial activity), separate authorization under this general permit if applicable, coverage under an alternative general permit if available, or authorization under an individual water quality permit.

3. Non-Storm Water Discharges

The following non-storm water discharges from sites authorized under this general permit are also eligible for authorization under this general permit:

- (a) discharges from fire fighting activities (fire fighting activities do not include washing of trucks, run-off water from training activities, test water from fire suppression systems, and similar activities);
- (b) uncontaminated fire hydrant flushings (excluding discharges of hyperchlorinated water, unless the water is first dechlorinated and discharges are not expected to adversely affect aquatic life), which include flushings from systems that utilize potable water, surface water, or groundwater that does not contain additional pollutants (uncontaminated fire hydrant flushings do not include systems utilizing reclaimed wastewater as a source water);
- (c) water from the routine external washing of vehicles, the external portion of buildings or structures, and pavement, where detergents and soaps are not used and where spills or leaks of toxic or hazardous materials have not occurred (unless spilled materials have been removed; and if local state, or federal regulations are applicable, the materials are removed according to those regulations), and where the purpose is to remove mud, dirt, or dust;
- (d) uncontaminated water used to control dust;

- (e) potable water sources including waterline flushings (excluding discharges of hyperchlorinated water, unless the water is first dechlorinated and discharges are not expected to adversely affect aquatic life);
 - (f) uncontaminated air conditioning condensate;
 - (g) uncontaminated ground water or spring water, including foundation or footing drains where flows are not contaminated with industrial materials such as solvents; and
 - (h) lawn watering and similar irrigation drainage.
4. Other Permitted Discharges

Any discharge authorized under a separate NPDES, TPDES, or TCEQ permit may be combined with discharges authorized by this general permit, provided those discharges comply with the associated permit.

Section B. Concrete Truck Wash Out

The washout of concrete trucks associated with off-site production facilities may be conducted at regulated construction sites in accordance with the requirements of Part V of this general permit.

Section C. Limitations on Permit Coverage

1. Post Construction Discharges.

Discharges that occur after construction activities have been completed, and after the construction site and any supporting activity site have undergone final stabilization, are not eligible for coverage under this general permit. Discharges originating from the sites are not authorized under this general permit following the submission of the notice of termination (NOT) for the construction activity.

2. Prohibition of Non-Storm Water Discharges

Except as otherwise provided in Part II.A. of this general permit, only discharges that are composed entirely of storm water associated with construction activity may be authorized under this general permit.

3. Compliance With Water Quality Standards

Discharges to surface water in the state that would cause or contribute to a violation of water quality standards or that would fail to protect and maintain existing designated uses are not eligible for coverage under this general permit. The executive director may require an application for an individual permit or alternative general permit (see Parts II.H.2. and 3.) to authorize discharges to surface water in the state from any activity that is determined to cause a violation of water quality standards or is found to cause, or contribute to, the loss of a designated use. The executive director may also require an application for an individual permit considering factors described in Part II.H.2. of this general permit.

4. Discharges to Water Quality-Impaired Receiving Waters.

New sources or new discharges of the constituents of concern to impaired waters are not authorized by this permit unless otherwise allowable under 30 TAC Chapter 305 and applicable state law. Impaired waters are those that do not meet applicable water quality standards and are listed on the EPA approved Clean Water Act Section 303(d) list. Constituents of concern are those for which the water body is listed as impaired.

Discharges of the constituents of concern to impaired water bodies for which there is a total maximum daily load (TMDL) are not eligible for this permit unless they are consistent with the approved TMDL. Permittees must incorporate the limitations, conditions, and requirements applicable to their discharges, including monitoring frequency and reporting required by TCEQ rules, into their storm water pollution prevention plan in order to be eligible for coverage under this general permit.

5. Discharges to the Edwards Aquifer Recharge Zone

Discharges cannot be authorized by this general permit where prohibited by 30 Texas Administrative Code (TAC) Chapter 213 (relating to Edwards Aquifer). **In addition, commencement of construction (i.e., the initial disturbance of soils associated with clearing, grading, or excavating activities, as well as other construction-related activities such as stockpiling of fill material and demolition) at a site regulated under 30 TAC Chapter 213, may not begin until the appropriate Edwards Aquifer Protection Plan has been approved by the TCEQ's Edwards Aquifer Protection Program.**

- (a) For new discharges located within the Edwards Aquifer Recharge Zone, or within that area upstream from the recharge zone and defined as the Contributing Zone, operators must meet all applicable requirements of, and operate according to, 30 TAC Chapter 213 (Edwards Aquifer Rule) in addition to the provisions and requirements of this general permit.
- (b) For existing discharges located within the Edwards Aquifer Recharge Zone, the requirements of the agency-approved Water Pollution Abatement Plan under the Edwards Aquifer Rules are in addition to the requirements of this general permit. BMPs and maintenance schedules for structural storm water controls, for example, may be required as a provision of the rule. All applicable requirements of the Edwards Aquifer Rule for reductions of suspended solids in storm water runoff are in addition to the requirements in this general permit for this pollutant.

For discharges from large construction activities located on the Edwards Aquifer recharge zone or the Edwards Aquifer contributing zone, applicants must submit a copy of the NOI to the appropriate TCEQ regional office. For discharges from small construction activities located on the Edwards Aquifer recharge zone or the Edwards Aquifer contributing zone, and for discharges from large construction activities by operators not required to submit an NOI under this general permit, applicants must submit a copy of the construction site notice to the appropriate TCEQ regional office where required by the Edwards Aquifer Rules at 30 TAC Chapter 213:

Counties:

Contact:

Comal, Bexar, Medina, Uvalde,
and Kinney

TCEQ
Water Program Manager
San Antonio Regional Office
14250 Judson Rd.
San Antonio, Texas
(210) 490-3096

Williamson, Travis, and Hays

TCEQ
Water Program Manager
Austin Regional Office
2800 South IH 35, Suite 100
Austin, Texas 78704-5712
(512) 339-2929

6. Discharges to Specific Watersheds and Water Quality Areas

Discharges otherwise eligible for coverage cannot be authorized by this general permit where prohibited by 30 TAC Chapter 311 (relating to Watershed Protection) for water quality areas and watersheds.

7. Protection of Streams and Watersheds by Other Governmental Entities

This general permit does not limit the authority or ability of federal, other state, or local governmental entities from placing additional or more stringent requirements on construction activities or discharges from construction activities. For example, this permit does not limit the authority of a home-rule municipality provided by Texas Local Government Code §401.002.

8. Indian Country Lands

Storm water runoff from construction activities occurring on Indian Country lands are not under the authority of the TCEQ and are not eligible for coverage under this general permit. If discharges of storm water require authorization under federal National Pollutant Discharge Elimination System (NPDES) regulations, authority for these discharges must be obtained from the U.S. Environmental Protection Agency (EPA).

9. Oil and Gas Production

Storm water runoff from construction activities associated with the exploration, development, or production of oil or gas or geothermal resources, including transportation of crude oil or natural gas by pipeline, are not under the authority of the TCEQ and are not eligible for coverage under this general permit. If discharges of storm water require authorization under federal NPDES regulations, authority for these discharges must be obtained from the EPA.

10. Storm Water Discharges from Agricultural Activities

Storm water discharges from agricultural activities that are not point source discharges of storm water are not subject to TPDES permit requirements. These activities may include clearing and cultivating ground for crops, construction of fences to contain livestock, construction of stock ponds, and other similar agricultural activities. Discharges of storm water runoff associated with the construction of facilities that are subject to TPDES regulations, such as the construction of confined animal feeding operations, would be point sources regulated under this general permit.

11. Other

Nothing in Part II of the general permit is intended to negate any person's ability to assert the force majeure (act of God, war, strike, riot, or other catastrophe) defenses found in 30 TAC § 70.7.

Section D. Deadlines for Obtaining Authorization to Discharge

1. Large Construction Activities

- (a) New Construction - Discharges from sites where the commencement of construction occurs on or after the effective date of this general permit must be authorized, either under this general permit or a separate TPDES permit, prior to the commencement of those construction activities.
- (b) Ongoing Construction - Operators of large construction activities continuing to operate after the effective date of this permit, and authorized under TPDES general permit TXR150000 (issued March 5, 2003), must submit an NOI to renew authorization under this general permit within 90 days of the effective date of this general permit. During this interim period, as a requirement of this TPDES permit, the operator must continue to meet the conditions and requirements of the previous TPDES permit.

2. Small Construction Activities

- (a) New Construction - Discharges from sites where the commencement of construction occurs on or after the effective date of this general permit must be authorized, either under this general permit or a separate TPDES permit, prior to the commencement of those construction activities.
- (b) Ongoing Construction - Discharges from ongoing small construction activities that commenced prior to the effective date of this general permit, and that would not meet the conditions to qualify for termination of this permit as described in Part II.E. of this general permit, must meet the requirements to be authorized, either under this general permit or a separate TPDES permit, within 90 days of the effective date of this general permit. During this interim period, as a requirement of this TPDES permit, the operator must continue to meet the conditions and requirements of the previous TPDES permit.

Section E. Obtaining Authorization to Discharge

1. Automatic Authorization for Small Construction Activities With Low Potential for Erosion:

If all of the following conditions are met, then a small construction activity is determined to occur during periods of low potential for erosion, and a site operator may be automatically authorized under this general permit without being required to develop a storm water pollution prevention plan or submit a notice of intent (NOI):

- (a) the construction activity occurs in a county listed in Appendix A;
- (b) the construction activity is initiated and completed, including either final or temporary stabilization of all disturbed areas, within the time frame identified in Appendix A for the location of the construction site;
- (c) all temporary stabilization is adequately maintained to effectively reduce or prohibit erosion, permanent stabilization activities have been initiated, and a condition of final stabilization is completed no later than 30 days following the end date of the time frame identified in Appendix A for the location of the construction site;
- (d) the permittee signs a completed construction site notice (Attachment 1 of this general permit), including the certification statement;
- (e) a signed copy of the construction site notice is posted at the construction site in a location where it is readily available for viewing by the general public, local, state, and federal authorities prior to commencing construction activities, and maintained in that location until completion of the construction activity;
- (f) a copy of the signed and certified construction site notice is provided to the operator of any municipal separate storm sewer system (MS4) receiving the discharge at least two days prior to commencement of construction activities;
- (g) any supporting concrete batch plant or asphalt batch plant is separately authorized for discharges of storm water runoff or other non-storm water discharges under an individual TPDES permit, another TPDES general permit, or under an individual TCEQ permit where storm water and non-storm water is disposed of by evaporation or irrigation (discharges are adjacent to water in the state); and
- (h) any non-storm water discharges are either authorized under a separate permit or authorization, or are not considered to be a wastewater.

Part II.G. of this general permit describes how an operator may apply for and obtain a waiver from permitting, for certain small construction activities that occur during a period with a low potential for erosion, where automatic authorization under this section is not available.

2. Automatic Authorization For All Other Small Construction Activities:

Operators of small construction activities not described in Part II.E.1. above may be automatically authorized under this general permit, and operators of these sites shall not be required to submit an NOI, provided that they meet all of the following conditions:

- (a) develop a SWP3 according to the provisions of this general permit, that covers either the entire site or all portions of the site for which the applicant is the operator, and implement that plan prior to commencing construction activities;
- (b) sign and certify a completed construction site notice (Attachment 2 of this general permit), post the notice at the construction site in a location where it is safely and readily available for viewing by the general public, local, state, and federal authorities, prior to commencing construction, and maintain the notice in that location until completion of the construction activity (for linear construction activities, e.g. pipeline or highway, the site notice must be placed in a publicly accessible location near where construction is actively underway; notice for these linear sites may be relocated, as necessary, along the length of the project, and the notice must be safely and readily available for viewing by the general public; local, state, and federal authorities); and
- (c) provide a copy of the signed and certified construction site notice to the operator of any municipal separate storm sewer system receiving the discharge at least two days prior to commencement of construction activities.

Operators of small construction activities as defined in Part I of this general permit shall not submit an NOI for coverage unless otherwise required by the executive director.

As described in Part I (Definitions) of this general permit, large construction activities include those that will disturb less than five (5) acres of land, but that are part of a larger common plan of development or sale that will ultimately disturb five (5) or more acres of land, and must meet the requirements of Part II.E.3. below.

3. Authorization for Large Construction Activities:

Operators of large construction activities that qualify for coverage under this general permit must meet all of the following conditions:

- (a) develop a SWP3 according to the provisions of this general permit that covers either the entire site or all portions of the site for which the applicant is the operator, and implement that plan prior to commencing construction activities;
- (b) primary operators must submit a Notice of Intent (NOI), using a form provided by the executive director, at least seven (7) days prior to commencing construction activities, or if utilizing electronic submittal, prior to commencing construction activities. If an additional primary operator is added after the initial NOI is submitted, the new primary operator must submit an NOI at least seven (7) days before assuming operational control, or if utilizing electronic NOI submittal, prior to assuming operational control. If the primary operator changes after the initial NOI is submitted, the new primary operator must submit a paper NOI or an electronic NOI at least ten (10) days before assuming operational control;
- (c) all primary operators must also post a copy of the signed NOI at the construction site in a location where it is readily available for viewing by the general public, local,

state, and federal authorities prior to commencing construction activities, and must maintain the NOI in that location until completion of the construction activity;

- (d) all operators of large construction activities must post a site notice in accordance with Part III.D.2. of this permit. The site notice must be located where it is safely and readily available for viewing by the general public, local, state, and federal authorities prior to commencing construction, and must be maintained in that location until completion of the construction activity (for linear construction activities, e.g. pipeline or highway, the site notice must be placed in a publicly accessible location near where construction is actively underway; notice for these linear sites may be relocated, as necessary, along the length of the project, and the notice must be safely and readily available for viewing by the general public; local, state, and federal authorities); and
 - (e) all primary operators must provide a copy of the signed NOI to the operator of any municipal separate storm sewer system (MS4) receiving the discharge and to any secondary operator, at least seven (7) days prior to commencing construction activities, and must list in the SWP3 the names and addresses of all MS4 operators receiving a copy.
 - (f) All persons meeting the definition of “secondary operator” in Part I of this permit are hereby notified that they are regulated under this general permit, but are not required to submit an NOI, provided that another operator(s) at the site has submitted an NOI, or is required to submit an NOI and the secondary operator has provided notification to the operator(s) of the need to obtain coverage (with records of notification available upon request). Any secondary operator notified under this provision may alternatively submit an NOI under this general permit, may seek coverage under an alternative TPDES individual permit, or may seek coverage under an alternative TPDES general permit if available.
4. Waivers for Small Construction Activities:

Part II.G. describes how operators of certain small construction activities may obtain a waiver from coverage.

5. Effective Date of Coverage

- (a) Operators of small construction activities as described in either Part II.E.1. or II.E.2. above are authorized immediately following compliance with the applicable conditions of Part II.E.1. or II.E.2. Secondary operators of large construction activities as described in Part II.E.3. above are authorized immediately following compliance with the applicable conditions in Part II.E.3. For activities located in areas regulated by 30 TAC Chapter 213, related to the Edwards Aquifer, this authorization to discharge is separate from the requirements of the operator’s responsibilities under that rule. Construction may not commence for sites regulated under 30 TAC Chapter 213 until all applicable requirements of that rule are met.
- (b) Primary operators of large construction activities as described in Part II.E.3. above are provisionally authorized seven (7) days from the date that a completed NOI is

postmarked for delivery to the TCEQ, unless otherwise notified by the executive director. If electronic submission of the NOI is provided, and unless otherwise notified by the executive director, primary operators are authorized immediately following confirmation of receipt of the NOI by the TCEQ. Authorization is non-provisional when the executive director finds the NOI is administratively complete and an authorization number is issued for the activity. For activities located in areas regulated by 30 TAC Chapter 213, related to the Edwards Aquifer, this authorization to discharge is separate from the requirements of the operator's responsibilities under that rule. Construction may not commence for sites regulated under 30 TAC Chapter 213 until all applicable requirements of that rule are met.

- (c) Operators are not prohibited from submitting late NOIs or posting late notices to obtain authorization under this general permit. The TCEQ reserves the right to take appropriate enforcement actions for any unpermitted activities that may have occurred between the time construction commenced and authorization was obtained.

6. Notice of Change (NOC)

If relevant information provided in the NOI changes, an NOC must be submitted at least 14 days before the change occurs, if possible. Where 14-day advance notice is not possible, the operator must submit an NOC within 14 days of discovery of the change. If the operator becomes aware that it failed to submit any relevant facts or submitted incorrect information in an NOI, the correct information must be provided to the executive director in an NOC within 14 days after discovery. The NOC shall be submitted on a form provided by the executive director, or by letter if an NOC form is not available. A copy of the NOC must also be provided to the operator of any MS4 receiving the discharge, and a list must be included in the SWP3 that includes the names and addresses of all MS4 operators receiving a copy.

Information that may be included on an NOC includes, but is not limited to, the following: the description of the construction project, an increase in the number of acres disturbed (for increases of one or more acres), or the operator name. A transfer of operational control from one operator to another, including a transfer of the ownership of a company, may not be included in an NOC. A transfer of ownership of a company includes changes to the structure of a company, such as changing from a partnership to a corporation or changing corporation types, so that the filing number (or charter number) that is on record with the Texas Secretary of State must be changed.

An NOC is not required for notifying TCEQ of a decrease in the number of acres disturbed. This information must be included in the storm water pollution prevention plan (SWP3) and retained on site.

7. Signatory Requirement for NOI Forms, Notice of Termination (NOT) Forms, NOC Letters, and Construction Site Notices

NOI forms, NOT forms, NOC letters, and Construction Site Notices that require a signature must be signed according to 30 TAC § 305.44 (relating to Signatories for Applications).

8. Contents of the NOI

The NOI form shall require, at a minimum, the following information:

- (a) the TPDES CGP authorization number for existing authorizations under this general permit, where the operator submits an NOI to renew coverage within 90 days of the effective date of this general permit;
- (b) the name, address, and telephone number of the operator filing the NOI for permit coverage;
- (c) the name (or other identifier), address, county, and latitude/longitude of the construction project or site;
- (d) the number of acres that will be disturbed by the applicant;
- (e) confirmation that the project or site will not be located on Indian Country lands;
- (f) confirmation that a SWP3 has been developed, that it will be implemented prior to construction, and that it is compliant with any applicable local sediment and erosion control plans;
- (g) name of the receiving water(s);
- (h) the classified segment number for each classified segment that receives discharges from the regulated construction activity (if the discharge is not directly to a classified segment, then the classified segment number of the first classified segment that those discharges reach); and
- (i) the name of all surface waters receiving discharges from the regulated construction activity that are on the latest EPA-approved CWA § 303(d) list of impaired waters.

Section F. Terminating Coverage

1. Notice of Termination (NOT) Required

Each operator that has submitted an NOI for authorization under this general permit must apply to terminate that authorization following the conditions described in this section of the general permit. Authorization must be terminated by submitting a Notice of Termination (NOT) on a form supplied by the executive director. Authorization to discharge under this general permit terminates at midnight on the day the NOT is postmarked for delivery to the TCEQ. If electronic submission of the NOT is provided, authorization to discharge under this permit terminates immediately following confirmation of receipt of the NOT by the TCEQ. Compliance with the conditions and requirements of this permit is required until an NOT is submitted.

The NOT must be submitted to TCEQ, and a copy of the NOT provided to the operator of any MS4 receiving the discharge (with a list in the SWP3 of the names and addresses of all MS4 operators receiving a copy), within 30 days after any of the following conditions are met:

- (a) final stabilization has been achieved on all portions of the site that are the responsibility of the permittee;
- (b) a transfer of operational control has occurred (See Section II.F.4. below); or
- (c) the operator has obtained alternative authorization under an individual TPDES permit or alternative TPDES general permit.

2. Minimum Contents of the NOT

The NOT form shall require, at a minimum, the following information:

- (a) if authorization was granted following submission of an NOI, the permittee's site-specific TPDES authorization number for the construction site;
- (b) an indication of whether the construction activity is completed or if the permittee is simply no longer an operator at the site;
- (c) the name, address, and telephone number of the permittee submitting the NOT;
- (d) the name (or other identifier), address, county, and latitude/longitude of the construction project or site; and
- (e) a signed certification that either all storm water discharges requiring authorization under this general permit will no longer occur, or that the applicant to terminate coverage is no longer the operator of the facility or construction site, and that all temporary structural erosion controls have either been removed, will be removed on a schedule defined in the SWP3, or have been transferred to a new operator if the new operator has applied for permit coverage. Erosion controls that are designed to remain in place for an indefinite period, such as mulches and fiber mats, are not required to be removed or scheduled for removal.

3. Termination of Coverage for Small Construction Sites and for Secondary Operators at Large Construction Sites

Each operator that has obtained automatic authorization and has not been required to submit an NOI must remove the site notice upon meeting any of the conditions listed below, complete the applicable portion of the site notice related to removal of the site notice, and submit a copy of the completed site notice to the operator of any MS4 receiving the discharge (or provide alternative notification as allowed by the MS4 operator, with documentation of such notification included in the SWP3), within 30 days of meeting any of the following conditions:

- (a) final stabilization has been achieved on all portions of the site that are the responsibility of the permittee;
- (b) a transfer of operational control has occurred (See Section II.F.4. below); or

- (c) the operator has obtained alternative authorization under an individual or general TPDES permit.

Authorization to discharge under this general permit terminates immediately upon removal of the applicable site notice. Compliance with the conditions and requirements of this permit is required until the site notice is removed.

4. Transfer of Operational Control

Coverage under this general permit is not transferable. A transfer of operational control includes changes to the structure of a company, such as changing from a partnership to a corporation, or changing to a different corporation type such that a different filing (or charter) number is established with the Texas Secretary of State.

When the primary operator of a large construction activity changes or operational control is transferred, the original operator must submit a Notice of Termination (NOT) within ten (10) days prior to the date that responsibility for operations terminates, and the new operator must submit an NOI at least ten (10) days prior to the transfer of operational control, in accordance with condition (a) or (b) below. A copy of the NOT must be provided to the operator of any MS4 receiving the discharge in accordance with Section II.F.1. above.

Operators of regulated construction activities who are not required to submit an NOI must remove the original site notice, and the new operator must post the required site notice prior to the transfer of operational control, in accordance with condition (a) or (b) below. A copy of the completed site notice must be provided to the operator of any MS4 receiving the discharge, in accordance with Section II.F.3. above.

A transfer of operational control occurs when either of the following criteria is met:

- (a) Another operator has assumed control over all areas of the site that have not been finally stabilized; and all silt fences and other temporary erosion controls have either been removed, scheduled for removal as defined in the SWP3, or transferred to a new operator, provided that the permitted operator has attempted to notify the new operator in writing of the requirement to obtain permit coverage. Record of this notification (or attempt at notification) shall be retained by the operator in accordance with Part VI of this permit. Erosion controls that are designed to remain in place for an indefinite period, such as mulches and fiber mats, are not required to be removed or scheduled for removal.
- (b) A homebuilder has purchased one or more lots from an operator who obtained coverage under this general permit for a common plan of development or sale. The homebuilder is considered a new operator and shall comply with the requirements listed above, including the development of a SWP3 if necessary. Under these circumstances, the homebuilder is only responsible for compliance with the general permit requirements as they apply to lot(s) it has operational control over, and the original operator remains responsible for common controls or discharges, and must amend its SWP3 to remove the lot(s) transferred to the homebuilder.

Section G. Waivers from Coverage

The executive director may waive the otherwise applicable requirements of this general permit for storm water discharges from small construction activities under the terms and conditions described in this section.

1. Waiver Applicability and Coverage

Operators of small construction activities may apply for and receive a waiver from the requirements to obtain authorization under this general permit, where all of the following conditions are met. This waiver from coverage does not apply to non-storm water discharges. The operator must insure that any non-storm water discharges are either authorized under a separate permit or authorization, or are not considered to be a wastewater.

- (a) the calculated rainfall erosivity (R) factor for the entire period of the construction project is less than five (5);
- (b) the operator submits to the TCEQ a signed waiver certification form, supplied by the executive director, certifying that the construction activity will commence and be completed within a period when the value of the calculated rainfall erosivity R factor is less than five (5); and
- (c) the waiver certification form is postmarked for delivery to the TCEQ at least two (2) days before construction activity begins.

2. Steps to Obtaining a Waiver

The construction site operator may calculate the R factor to request a waiver using the following steps:

- (a) Estimate the construction start date and the construction end date. The construction end date is the date that final stabilization will be achieved.
- (b) Find the appropriate Erosivity Index (EI) zone in Appendix B of this permit.
- (c) Find the EI percentage for the project period by adding the results for each period of the project using the table provided in Appendix D of this permit, in EPA Fact Sheet 2.1, or in USDA Handbook 703, by subtracting the start value from the end value to find the percent EI for the site.
- (d) Refer to the Isoerodent Map (Appendix C of this permit) and interpolate the annual isoerodent value for the proposed construction location.
- (e) Multiply the percent value obtained in Step (c) above by the annual isoerodent value obtained in Step (d). This is the R factor for the proposed project. If the value is less than 5, then a waiver may be obtained. If the value is five (5) or more, then a waiver may not be obtained, and the operator must obtain coverage under Part II.E.2. of this permit.

Alternatively, the operator may calculate a site-specific R factor utilizing the following online calculator: <http://ei.tamu.edu/index.html>, or using another available resource.

The waiver certification form is not required to be posted at the small construction site.

3. Effective Date of Waiver

Operators of small construction activities are provisionally waived from the otherwise applicable requirements of this general permit two (2) days from the date that a completed waiver certification form is postmarked for delivery to TCEQ.

4. Activities Extending Beyond the Waiver Period

If a construction activity extends beyond the approved waiver period due to circumstances beyond the control of the operator, the operator must either:

- (a) recalculate the rainfall erosivity (R) factor using the original start date and a new projected ending date, and if the R factor is still under five (5), submit a new waiver certification form at least two (2) days before the end of the original waiver period; or
- (b) obtain authorization under this general permit according to the requirements delineated in either Part II.E.2. or Part II.E.3. at least two (2) days before the end of the approved waiver period.

Section H. Alternative TPDES Permit Coverage

1. Individual Permit Alternative

Any discharge eligible for coverage under this general permit may alternatively be authorized under an individual TPDES permit according to 30 TAC Chapter 305 (relating to Consolidated Permits). Applications for individual permit coverage should be submitted at least three hundred and thirty (330) days prior to commencement of construction activities to ensure timely issuance.

2. Individual Permit Required

The executive director may suspend an authorization or deny an NOI in accordance with the procedures set forth in 30 TAC Chapter 205 (relating to General Permits for Waste Discharges), including the requirement that the executive director provide written notice to the permittee. The executive director may require an operator of a construction site, otherwise eligible for authorization under this general permit, to apply for an individual TPDES permit in the following circumstances:

- (a) the conditions of an approved total maximum daily load (TMDL) limitation or TMDL implementation plan on the receiving stream;

- (b) the activity being determined to cause a violation of water quality standards or being found to cause, or contribute to, the loss of a designated use of surface water in the state: and
- (c) any other consideration defined in 30 TAC Chapter 205 (relating to General Permits for Waste Discharges) including 30 TAC §205.4(c)(3)(D), which allows the commission to deny authorization under the general permit and require an individual permit if a discharger “has been determined by the executive director to have been out of compliance with any rule, order, or permit of the commission, including non-payment of fees assessed by the executive director.”

Additionally, the executive director may cancel, revoke, or suspend authorization to discharge under this general permit based on a finding of historical and significant noncompliance with the provisions of this general permit, relating to 30 TAC §60.3 (Use of Compliance History). Denial of authorization to discharge under this general permit or suspension of a permittee’s authorization under this general permit shall be done according to commission rules in 30 TAC, Chapter 205 (relating to General Permits for Waste Discharges).

- 3. Any discharge eligible for authorization under this general permit may alternatively be authorized under a separate general permit according to 30 TAC Chapter 205 (relating to General Permits for Waste Discharges), if applicable.

Section I. Permit Expiration

- 1. This general permit is issued for a term not to exceed five (5) years. All active discharge authorizations expire on the date provided on page one (1) of this permit. Following public notice and comment, as provided by 30 TAC §205.3 (relating to Public Notice, Public Meetings, and Public Comment), the commission may amend, revoke, cancel, or renew this general permit.
- 2. If the executive director publishes a notice of the intent to renew or amend this general permit before the expiration date, the permit will remain in effect for existing, authorized discharges until the commission takes final action on the permit. Upon issuance of a renewed or amended permit, permittees may be required to submit an NOI within 90 days following the effective date of the renewed or amended permit, unless that permit provides for an alternative method for obtaining authorization.
- 3. If the commission does not propose to reissue this general permit within 90 days before the expiration date, permittees shall apply for authorization under an individual permit or an alternative general permit. If the application for an individual permit is submitted before the expiration date, authorization under this expiring general permit remains in effect until the issuance or denial of an individual permit. No new NOIs will be accepted nor new authorizations honored under the general permit after the expiration date.

Part III. Storm Water Pollution Prevention Plans (SWP3)

Storm water pollution prevention plans must be prepared to address discharges authorized under Parts II.E.2. and II.E.3. that will reach Waters of the United States, including discharges to MS4s and privately owned

separate storm sewer systems that drain to Waters of the United States, to identify and address potential sources of pollution that are reasonably expected to affect the quality of discharges from the construction site, including off-site material storage areas, overburden and stockpiles of dirt, borrow areas, equipment staging areas, vehicle repair areas, fueling areas, etc., used solely by the permitted project. The SWP3 must describe the implementation of practices that will be used to minimize to the extent practicable the discharge of pollutants in storm water associated with construction activity and non-storm water discharges described in Part II.A.3., in compliance with the terms and conditions of this permit.

Individual operators at a site may develop separate SWP3s that cover only their portion of the project, provided reference is made to the other operators at the site. Where there is more than one SWP3 for a site, permittees must coordinate to ensure that BMPs and controls are consistent and do not negate or impair the effectiveness of each other. Regardless of whether a single comprehensive SWP3 is developed or separate SWP3s are developed for each operator, it is the responsibility of each operator to ensure compliance with the terms and conditions of this general permit in the areas of the construction site where that operator has control over construction plans and specifications or day-to-day operations.

Section A. Shared SWP3 Development

For more effective coordination of BMPs and opportunities for cost sharing, a cooperative effort by the different operators at a site is encouraged. Operators must independently obtain authorization, but may work together to prepare and implement a single, comprehensive SWP3 for the entire construction site.

1. The SWP3 must clearly list the name and, for large construction activities, the general permit authorization numbers, for each operator that participates in the shared SWP3. Until the TCEQ responds to receipt of the NOI with a general permit authorization number, the SWP3 must specify the date that the NOI was submitted to TCEQ by each operator. Each operator participating in the shared plan must also sign the SWP3.
2. The SWP3 must clearly indicate which operator is responsible for satisfying each shared requirement of the SWP3. If the responsibility for satisfying a requirement is not described in the plan, then each permittee is entirely responsible for meeting the requirement within the boundaries of the construction site where they perform construction activities. The SWP3 must clearly describe responsibilities for meeting each requirement in shared or common areas.

Section B. Responsibilities of Operators

1. Secondary Operators and Primary Operators with Control Over Construction Plans and Specifications

All secondary operators and primary operators with control over construction plans and specifications must:

- (a) ensure the project specifications allow or provide that adequate BMPs are developed to meet the requirements of Part III of this general permit;
- (b) ensure that the SWP3 indicates the areas of the project where they have control over project specifications, including the ability to make modifications in specifications;

- (c) ensure all other operators affected by modifications in project specifications are notified in a timely manner so that those operators may modify their best management practices as necessary to remain compliant with the conditions of this general permit; and
 - (d) ensure that the SWP3 for portions of the project where they are operators indicates the name and site-specific TPDES authorization numbers for permittees with the day-to-day operational control over those activities necessary to ensure compliance with the SWP3 and other permit conditions. If the party with day-to-day operational control has not been authorized or has abandoned the site, the person with control over project specifications is considered to be the responsible party until the authority is transferred to another party and the SWP3 is updated.
2. Primary Operators with Day-to-Day Operational Control

Primary Operators with day-to-day operational control of those activities at a project that are necessary to ensure compliance with an SWP3 and other permit conditions must ensure that the SWP3 accomplishes the following requirements:

- (a) meets the requirements of this general permit for those portions of the project where they are operators;
- (b) identifies the parties responsible for implementation of best management practices (BMPs) described in the SWP3;
- (c) indicates areas of the project where they have operational control over day-to-day activities; and
- (d) includes, for areas where they have operational control over day-to-day activities, the name and site-specific TPDES authorization number of the parties with control over project specifications, including the ability to make modifications in specifications.

Section C. Deadlines for SWP3 Preparation, Implementation, and Compliance

The SWP3 must be prepared prior to obtaining authorization under this general permit, and implemented prior to commencing construction activities that result in soil disturbance. The SWP3 must be prepared so that it provides for compliance with the terms and conditions of this general permit.

Section D. Plan Review and Making Plans Available

1. The SWP3 must be retained on-site at the construction site or, if the site is inactive or does not have an on-site location to store the plan, a notice must be posted describing the location of the SWP3. The SWP3 must be made readily available at the time of an on-site inspection to: the executive director; a federal, state, or local agency approving sediment and erosion plans, grading plans, or storm water management plans; local government officials; and the operator of a municipal separate storm sewer receiving discharges from the site.

2. In addition to the requirement to post the NOI, a primary operator of a large construction activity must post the site notice provided in Attachment 4 of this permit near the main entrance of the construction site. An operator of a small construction activity seeking authorization under this general permit and a secondary operator of a large construction activity must post the site notice required in Part II.E.1., 2., or 3. of this permit in order to obtain authorization (see Attachments 1, 2, and 3). If the construction project is a linear construction project (e.g. pipeline or highway), the notices must be placed in a publicly accessible location near where construction is actively underway. Notices for these linear sites may be relocated, as necessary, along the length of the project. The notices must be readily available for viewing by the general public; local, state, and federal authorities; and contain the following information:
 - (a) the site-specific TPDES authorization number for the project if assigned;
 - (b) the operator name, contact name, and contact phone number;
 - (c) a brief description of the project; and
 - (d) the location of the SWP3.
3. This permit does not provide the general public with any right to trespass on a construction site for any reason, including inspection of a site; nor does this permit require that permittees allow members of the general public access to a construction site.

Section E. Revisions and Updates to SWP3s

The permittee must revise or update the SWP3 whenever the following occurs:

1. a change in design, construction, operation, or maintenance that has a significant effect on the discharge of pollutants and that has not been previously addressed in the SWP3;
2. changing site conditions based on updated plans and specifications, new operators, new areas of responsibility, and changes in BMPs; or
3. results of inspections or investigations by site operators, operators of a municipal separate storm sewer system receiving the discharge, authorized TCEQ personnel, or a federal, state or local agency approving sediment and erosion plans indicate the SWP3 is proving ineffective in eliminating or significantly minimizing pollutants in discharges authorized under this general permit.

Section F. Contents of SWP3

The SWP3 must include, at a minimum, the information described in this section.

1. A site or project description, which includes the following information:
 - (a) a description of the nature of the construction activity;
 - (b) a list of potential pollutants and their sources;

- (c) a description of the intended schedule or sequence of activities that will disturb soils for major portions of the site;
- (d) the total number of acres of the entire property and the total number of acres where construction activities will occur, including off-site material storage areas, overburden and stockpiles of dirt, and borrow areas that are authorized under the permittee's NOI;
- (e) data describing the soil or the quality of any discharge from the site;
- (f) a map showing the general location of the site (e.g. a portion of a city or county map);
- (g) a detailed site map (or maps) indicating the following:
 - (i) drainage patterns and approximate slopes anticipated after major grading activities;
 - (ii) areas where soil disturbance will occur;
 - (iii) locations of all major structural controls either planned or in place;
 - (iv) locations where temporary or permanent stabilization practices are expected to be used;
 - (v) locations of construction support activities, including off-site activities, that are authorized under the permittee's NOI, including material, waste, borrow, fill, or equipment storage areas;
 - (vi) surface waters (including wetlands) either at, adjacent, or in close proximity to the site;
 - (vii) locations where storm water discharges from the site directly to a surface water body or a municipal separate storm sewer system; and
 - (viii) vehicle wash areas.

Where the amount of information required to be included on the map would result in a single map being difficult to read and interpret, the operator shall develop a series of maps that collectively include the required information.

- (h) the location and description of support activities authorized under the permittee's NOI, including asphalt plants, concrete plants, and other activities providing support to the construction site that is authorized under this general permit;
- (i) the name of receiving waters at or near the site that may be disturbed or that may receive discharges from disturbed areas of the project;

- (j) a copy of this TPDES general permit, and
 - (k) the notice of intent (NOI) and acknowledgement certificate for primary operators of large construction sites, and the site notice for small construction sites and for secondary operators of large construction sites.
2. A description of the best management practices (BMPs) that will be used to minimize pollution in runoff.

The description must identify the general timing or sequence for implementation. At a minimum, the description must include the following components:

(a) General Requirements

- (i) Erosion and sediment controls must be designed to retain sediment on-site to the extent practicable with consideration for local topography, soil type, and rainfall.
- (ii) Control measures must be properly selected, installed, and maintained according to the manufacturer's or designer's specifications.
- (iii) Controls must be developed to minimize the offsite transport of litter, construction debris, and construction materials.

(b) Erosion Control and Stabilization Practices

The SWP3 must include a description of temporary and permanent erosion control and stabilization practices for the site, including a schedule of when the practices will be implemented. Site plans should ensure that existing vegetation is preserved where it is possible.

- (i) Erosion control and stabilization practices may include but are not limited to: establishment of temporary or permanent vegetation, mulching, geotextiles, sod stabilization, vegetative buffer strips, protection of existing trees and vegetation, slope texturing, temporary velocity dissipation devices, flow diversion mechanisms, and other similar measures.
- (ii) The following records must be maintained and either attached to or referenced in the SWP3, and made readily available upon request to the parties listed in Part III.D.1 of this general permit:
 - (A) the dates when major grading activities occur;
 - (B) the dates when construction activities temporarily or permanently cease on a portion of the site; and
 - (C) the dates when stabilization measures are initiated.

- (iii) Erosion control and stabilization measures must be initiated as soon as practicable in portions of the site where construction activities have temporarily ceased. Stabilization measures that provide a protective cover must be initiated as soon as practicable in portions of the site where construction activities have permanently ceased. Except as provided in (A) through (D) below, these measures must be initiated no more than 14 days after the construction activity in that portion of the site has temporarily or permanently ceased:
 - (A) Where the initiation of stabilization measures by the 14th day after construction activity temporarily or permanently ceased is precluded by snow cover or frozen ground conditions, stabilization measures must be initiated as soon as practicable.
 - (B) Where construction activity on a portion of the site has temporarily ceased, and earth disturbing activities will be resumed within 21 days, temporary erosion control and stabilization measures are not required on that portion of site.
 - (C) In arid areas, semiarid areas, and areas experiencing droughts where the initiation of stabilization measures by the 14th day after construction activity has temporarily or permanently ceased or is precluded by arid conditions, erosion control and stabilization measures must be initiated as soon as practicable. Where vegetative controls are not feasible due to arid conditions, the operator shall install non-vegetative erosion controls. If non-vegetative controls are not feasible, the operator shall install temporary sediment controls as required in Paragraph (D) below.
 - (D) In areas where temporary stabilization measures are infeasible, the operator may alternatively utilize temporary perimeter controls. The operator must document in the SWP3 the reason why stabilization measures are not feasible, and must demonstrate that the perimeter controls will retain sediment on site to the extent practicable. The operator must continue to inspect the BMPs at the frequency established in Section III.F.7.(a) for unstabilized sites.
 - (iv) Final stabilization must be achieved prior to termination of permit coverage.
- (c) Sediment Control Practices

The SWP3 must include a description of any sediment control practices used to remove eroded soils from storm water runoff, including the general timing or sequence for implementation of controls.

- (i) Sites With Drainage Areas of Ten or More Acres
 - (A) Sedimentation Basin(s)

- (1) A sedimentation basin is required, where feasible, for a common drainage location that serves an area with ten (10) or more acres disturbed at one time. A sedimentation basin may be temporary or permanent, and must provide sufficient storage to contain a calculated volume of runoff from a 2-year, 24-hour storm from each disturbed acre drained. When calculating the volume of runoff from a 2-year, 24-hour storm event, it is not required to include the flows from offsite areas and flow from onsite areas that are either undisturbed or have already undergone permanent stabilization, if these flows are diverted around both the disturbed areas of the site and the sediment basin. Capacity calculations shall be included in the SWP3.
 - (2) Where rainfall data is not available or a calculation cannot be performed, the sedimentation basin must provide at least 3,600 cubic feet of storage per acre drained until final stabilization of the site.
 - (3) If a sedimentation basin is not feasible, then the permittee shall provide equivalent control measures until final stabilization of the site. In determining whether installing a sediment basin is feasible, the permittee may consider factors such as site soils, slope, available area, public safety, precipitation patterns, site geometry, site vegetation, infiltration capacity, geotechnical factors, depth to groundwater, and other similar considerations. The permittee shall document the reason that the sediment basins are not feasible, and shall utilize equivalent control measures, which may include a series of smaller sediment basins.
- (B) Perimeter Controls: At a minimum, silt fences, vegetative buffer strips, or equivalent sediment controls are required for all down slope boundaries of the construction area, and for those side slope boundaries deemed appropriate as dictated by individual site conditions.
- (ii) Controls for Sites With Drainage Areas Less than Ten Acres:
- (A) Sediment traps and sediment basins may be used to control solids in storm water runoff for drainage locations serving less than ten (10) acres. At a minimum, silt fences, vegetative buffer strips, or equivalent sediment controls are required for all down slope boundaries of the construction area, and for those side slope boundaries deemed appropriate as dictated by individual site conditions.
 - (B) Alternatively, a sediment basin that provides storage for a calculated volume of runoff from a 2-year, 24-hour storm from each disturbed

acre drained may be utilized. Where rainfall data is not available or a calculation cannot be performed, a temporary or permanent sediment basin providing 3,600 cubic feet of storage per acre drained may be provided. If a calculation is performed, then the calculation shall be included in the SWP3.

3. A Description of Permanent Storm Water Controls

A description of any measures that will be installed during the construction process to control pollutants in storm water discharges that may occur after construction operations have been completed must be included in the SWP3. Permittees are only responsible for the installation and maintenance of storm water management measures prior to final stabilization of the site or prior to submission of an NOT.

4. Other Required Controls and BMPs

- (a) Permittees shall minimize, to the extent practicable, the off-site vehicle tracking of sediments and the generation of dust. The SWP3 shall include a description of controls utilized to accomplish this requirement.
- (b) The SWP3 must include a description of construction and waste materials expected to be stored on-site and a description of controls to minimize pollutants from these materials.
- (c) The SWP3 must include a description of potential pollutant sources from areas other than construction (such as storm water discharges from dedicated asphalt plants and dedicated concrete batch plants), and a description of controls and measures that will be implemented at those sites to minimize pollutant discharges.
- (d) Permittees shall place velocity dissipation devices at discharge locations and along the length of any outfall channel (i.e., runoff conveyance) to provide a non-erosive flow velocity from the structure to a water course, so that the natural physical and biological characteristics and functions are maintained and protected.
- (e) Permittees shall design and utilize appropriate controls to minimize the offsite transport of suspended sediments and other pollutants if it is necessary to pump or channel standing water from the site.

5. Documentation of Compliance with Approved State and Local Plans

- (a) Permittees must ensure that the SWP3 is consistent with requirements specified in applicable sediment and erosion site plans or site permits, or storm water management site plans or site permits approved by federal, state, or local officials.
- (b) SWP3s must be updated as necessary to remain consistent with any changes applicable to protecting surface water resources in sediment erosion site plans or site permits, or storm water management site plans or site permits approved by state or local official for which the permittee receives written notice.

- (c) If the permittee is required to prepare a separate management plan, including but not limited to a Water Pollution Abatement Plan or Contributing Zone Plan in accordance with 30 TAC Chapter 213 (related to the Edwards Aquifer), then a copy of that plan must be either included in the SWP3 or made readily available upon request to authorized personnel of the TCEQ. The permittee shall maintain a copy of the approval letter for the plan in its SWP3.

6. Maintenance Requirements

- (a) All protective measures identified in the SWP3 must be maintained in effective operating condition. If, through inspections or other means, the permittee determines that BMPs are not operating effectively, then the permittee shall perform maintenance as necessary to maintain the continued effectiveness of storm water controls, and prior to the next rain event if feasible. If maintenance prior to the next anticipated storm event is impracticable, the reason shall be documented in the SWP3 and maintenance must be scheduled and accomplished as soon as practicable. Erosion and sediment controls that have been intentionally disabled, run-over, removed, or otherwise rendered ineffective must be replaced or corrected immediately upon discovery.
- (b) If periodic inspections or other information indicates a control has been used incorrectly, is performing inadequately, or is damaged, then the operator must replace or modify the control as soon as practicable after making the discovery.
- (c) Sediment must be removed from sediment traps and sedimentation ponds no later than the time that design capacity has been reduced by 50%. For perimeter controls such as silt fences, berms, etc., the trapped sediment must be removed before it reaches 50% of the above-ground height.
- (d) If sediment escapes the site, accumulations must be removed at a frequency that minimizes off-site impacts, and prior to the next rain event, if feasible. If the permittee does not own or operate the off-site conveyance, then the permittee must work with the owner or operator of the property to remove the sediment.

7. Inspections of Controls

- (a) Personnel provided by the permittee must inspect disturbed areas of the construction site that have not been finally stabilized, areas used for storage of materials that are exposed to precipitation, discharge locations, and structural controls for evidence of, or the potential for, pollutants entering the drainage system. Personnel conducting these inspections must be knowledgeable of this general permit, familiar with the construction site, and knowledgeable of the SWP3 for the site. Sediment and erosion control measures identified in the SWP3 must be inspected to ensure that they are operating correctly. Locations where vehicles enter or exit the site must be inspected for evidence of off-site sediment tracking. Inspections must be conducted at least once every 14 calendar days and within 24 hours of the end of a storm event of 0.5 inches or greater.

Where sites have been finally or temporarily stabilized or where runoff is unlikely due to winter conditions (e.g. site is covered with snow, ice, or frozen ground exists), inspections must be conducted at least once every month. In arid or semi-arid areas, inspections must be conducted at least once every month and within 24 hours after the end of a storm event of 0.5 inches or greater.

As an alternative to the above-described inspection schedule of once every 14 calendar days and within 24 hours of a storm event of 0.5 inches or greater, the SWP3 may be developed to require that these inspections will occur at least once every seven (7) calendar days. If this alternative schedule is developed, then the inspection must occur on a specifically defined day, regardless of whether or not there has been a rainfall event since the previous inspection. The inspections may occur on either schedule provided that the SWP3 reflects the current schedule and that any changes to the schedule are conducted in accordance with the following provisions: the schedule may be changed a maximum of one time each month, the schedule change must be implemented at the beginning of a calendar month, and the reason for the schedule change must be documented in the SWP3 (e.g., end of “dry” season and beginning of “wet” season).

- (b) Utility line installation, pipeline construction, and other examples of long, narrow, linear construction activities may provide inspection personnel with limited access to the areas described in Part III.F.8.(a) above. Inspection of these areas could require that vehicles compromise temporarily or even permanently stabilized areas, cause additional disturbance of soils, and increase the potential for erosion. In these circumstances, controls must be inspected at least once every 14 calendar days and within 24 hours of the end of a storm event of 0.5 inches, but representative inspections may be performed. For representative inspections, personnel must inspect controls along the construction site for 0.25 mile above and below each access point where a roadway, undisturbed right-of-way, or other similar feature intersects the construction site and allows access to the areas described in Part III.F.8.(a) above. The conditions of the controls along each inspected 0.25 mile portion may be considered as representative of the condition of controls along that reach extending from the end of the 0.25 mile portion to either the end of the next 0.25 mile inspected portion, or to the end of the project, whichever occurs first.

As an alternative to the above-described inspection schedule of once every 14 calendar days and within 24 hours of a storm event of 0.5 inches or greater, the SWP3 may be developed to require that these inspections will occur at least once every seven (7) calendar days. If this alternative schedule is developed, the inspection must occur on a specifically defined day, regardless of whether or not there has been a rainfall event since the previous inspection. The inspections may occur on either schedule provided that the SWP3 reflects the current schedule and that any changes to the schedule are conducted in accordance with the following provisions: the schedule may be changed a maximum of one time each month, the schedule change must be implemented at the beginning of a calendar month, and the reason for the schedule change must be documented in the SWP3 (e.g., end of “dry” season and beginning of “wet” season).

- (c) In the event of flooding or other uncontrollable situations which prohibit access to the inspection sites, inspections must be conducted as soon as access is practicable.
- (d) The SWP3 must be modified based on the results of inspections, as necessary, to better control pollutants in runoff. Revisions to the SWP3 must be completed within seven (7) calendar days following the inspection. If existing BMPs are modified or if additional BMPs are necessary, an implementation schedule must be described in the SWP3 and wherever possible those changes implemented before the next storm event. If implementation before the next anticipated storm event is impracticable, these changes must be implemented as soon as practicable.
- (e) A report summarizing the scope of the inspection, the date(s) of the inspection, and major observations relating to the implementation of the SWP3 must be made and retained as part of the SWP3. Major observations should include: The locations of discharges of sediment or other pollutants from the site; locations of BMPs that need to be maintained; locations of BMPs that failed to operate as designed or proved inadequate for a particular location; and locations where additional BMPs are needed.

Actions taken as a result of inspections must be described within, and retained as a part of, the SWP3. Reports must identify any incidents of non-compliance. Where a report does not identify any incidents of non-compliance, the report must contain a certification that the facility or site is in compliance with the SWP3 and this permit. The report must be signed by the person and in the manner required by 30 TAC § 305.128 (relating to Signatories to Reports).

The names and qualifications of personnel making the inspections for the permittee may be documented once in the SWP3 rather than being included in each report.

- 8. The SWP3 must identify and ensure the implementation of appropriate pollution prevention measures for all eligible non-storm water components of the discharge, as listed in Part II.A.3. of this permit.
- 9. The SWP3 must include the information required in Part III.B. of this general permit.

Part IV. Storm Water Runoff from Concrete Batch Plants

Discharges of storm water runoff from concrete batch plants at regulated construction sites may be authorized under the provisions of this general permit provided that the following requirements are met for concrete batch plant(s) authorized under this permit. If discharges of storm water runoff from concrete batch plants are not covered under this general permit, then discharges must be authorized under an alternative general permit or individual permit. This permit does not authorize the discharge or land disposal of any wastewater from concrete batch plants at regulated construction sites. Authorization for these wastes must be obtained under an individual permit or an alternative general permit.

Section A. Benchmark Sampling Requirements

- 1. Operators of concrete batch plants authorized under this general permit must sample the storm water runoff from the concrete batch plants according to the requirements of this

section of this general permit, and must conduct evaluations on the effectiveness of the SWP3 based on the following benchmark monitoring values:

Benchmark Parameter	Benchmark Value	Sampling Frequency	Sample Type
Oil and Grease	15 mg/L	1/quarter (*1)(*2)	Grab (*3)
Total Suspended Solids	100 mg/L	1/quarter (*1)(*2)	Grab (*3)
pH	6.0 - 9.0 Standard Units	1/quarter (*1)(*2)	Grab (*3)
Total Iron	1.3 mg/L	1/quarter(*1)(*2)	Grab (*3)

(*1) When discharge occurs. Sampling is required within the first 30 minutes of discharge. If it is not practicable to take the sample, or to complete the sampling, within the first 30 minutes, sampling must be completed within the first hour of discharge. If sampling is not completed within the first 30 minutes of discharge, the reason must be documented and attached to all required reports and records of the sampling activity.

(*2) Sampling must be conducted at least once during each of the following periods. The first sample must be collected during the first full quarter that a storm water discharge occurs from a concrete batch plant authorized under this general permit.

- January through March
- April through June
- July through September
- October through December

For projects lasting less than one full quarter, a minimum of one sample shall be collected, provided that a storm water discharge occurred at least once following submission of the NOI or following the date that automatic authorization was obtained under Section II.E.2., and prior to terminating coverage.

(*3) A grab sample shall be collected from the storm water discharge resulting from a storm event that is at least 0.1 inches of measured precipitation that occurs at least 72 hours from the previously measurable storm event. The sample shall be collected downstream of the concrete batch plant, and where the discharge exits any BMPs utilized to handle the runoff from the batch plant, prior to commingling with any other water authorized under this general permit.

2. The permittee must compare the results of sample analyses to the benchmark values above, and must include this comparison in the overall assessment of the SWP3’s effectiveness. Analytical results that exceed a benchmark value are not a violation of this permit, as these values are not numeric effluent limitations. Results of analyses are indicators that modifications of the SWP3 should be assessed and may be necessary to protect water quality. The operator must investigate the cause for each exceedance and must document the results of this investigation in the SWP3 by the end of the quarter following the sampling event.

The operator's investigation must identify the following:

- (a) any additional potential sources of pollution, such as spills that might have occurred,
- (b) necessary revisions to good housekeeping measures that are part of the SWP3,
- (c) additional BMPs, including a schedule to install or implement the BMPs, and
- (d) other parts of the SWP3 that may require revisions in order to meet the goal of the benchmark values.

Background concentrations of specific pollutants may also be considered during the investigation. If the operator is able to relate the cause of the exceedance to background concentrations, then subsequent exceedances of benchmark values for that pollutant may be resolved by referencing earlier findings in the SWP3. Background concentrations may be identified by laboratory analyses of samples of storm water runoff to the permitted facility, by laboratory analyses of samples of storm water run-off from adjacent non-industrial areas, or by identifying the pollutant is a naturally occurring material in soils at the site.

Section B. Best Management Practices (BMPs) and SWP3 Requirements

Minimum Storm Water Pollution Prevention Plan (SWP3) Requirements – The following are required in addition to other SWP3 requirements listed in this general permit (including, but not limited to Part III.F.7. of this permit):

1. Description of Potential Pollutant Sources - The SWP3 must provide a description of potential sources (activities and materials) that may reasonably be expected to affect the quality of storm water discharges associated with concrete batch plants authorized under this permit. The SWP3 must describe practices that that will be used to reduce the pollutants in these discharges to assure compliance with this general permit, including the protection of water quality, and must ensure the implementation of these practices.

The following must be developed, at a minimum, in support of developing this description:

- (a) Drainage – The site map must include the following information:
 - (1) the location of all outfalls for storm water discharges associated with concrete batch plants that are authorized under this permit;
 - (2) a depiction of the drainage area and the direction of flow to the outfall(s);
 - (3) structural controls used within the drainage area(s);
 - (4) the locations of the following areas associated with concrete batch plants that are exposed to precipitation: vehicle and equipment maintenance activities (including fueling, repair, and storage areas for vehicles and equipment scheduled for maintenance); areas used for the treatment, storage, or disposal

of wastes; liquid storage tanks; material processing and storage areas; and loading and unloading areas; and

- (5) the locations of the following: any bag house or other dust control device(s); recycle/sedimentation pond, clarifier or other device used for the treatment of facility wastewater (including the areas that drain to the treatment device); areas with significant materials; and areas where major spills or leaks have occurred.
 - (b) Inventory of Exposed Materials – A list of materials handled at the concrete batch plant that may be exposed to storm water and that have a potential to affect the quality of storm water discharges associated with concrete batch plants that are authorized under this general permit.
 - (c) Spills and Leaks - A list of significant spills and leaks of toxic or hazardous pollutants that occurred in areas exposed to storm water and that drain to storm water outfalls associated with concrete batch plants authorized under this general permit must be developed, maintained, and updated.
 - (d) Sampling Data - A summary of existing storm water discharge sampling data must be maintained, if available.
2. Measures and Controls - The SWP3 must include a description of management controls to regulate pollutants identified in the SWP3's "Description of Potential Pollutant Sources" from Part IV.B.1.(a) of this permit, and a schedule for implementation of the measures and controls. This must include, at a minimum:
- (a) Good Housekeeping - Good housekeeping measures must be developed and implemented in the area(s) associated with concrete batch plants.
 - (1) Operators must prevent or minimize the discharge of spilled cement, aggregate (including sand or gravel), settled dust, or other significant materials from paved portions of the site that are exposed to storm water. Measures used to minimize the presence of these materials may include regular sweeping or other equivalent practices. These practices must be conducted at a frequency that is determined based on consideration of the amount of industrial activity occurring in the area and frequency of precipitation, and shall occur at least once per week when cement or aggregate is being handled or otherwise processed in the area.
 - (2) Operators must prevent the exposure of fine granular solids, such as cement, to storm water. Where practicable, these materials must be stored in enclosed silos, hoppers or buildings, in covered areas, or under covering.
 - (b) Spill Prevention and Response Procedures - Areas where potential spills that can contribute pollutants to storm water runoff, and the drainage areas from these locations, must be identified in the SWP3. Where appropriate, the SWP3 must specify material handling procedures, storage requirements, and use of equipment.

Procedures for cleaning up spills must be identified in the SWP3 and made available to the appropriate personnel.

- (c) Inspections - Qualified facility personnel (i.e., a person or persons with knowledge of this general permit, the concrete batch plant, and the SWP3 related to the concrete batch plant(s) for the site) must be identified to inspect designated equipment and areas of the facility specified in the SWP3. The inspection frequency must be specified in the SWP3 based upon a consideration of the level of concrete production at the facility, but must be a minimum of once per month while the facility is in operation. The inspection must take place while the facility is in operation and must, at a minimum, include all areas that are exposed to storm water at the site, including material handling areas, above ground storage tanks, hoppers or silos, dust collection/containment systems, truck wash down and equipment cleaning areas. Follow-up procedures must be used to ensure that appropriate actions are taken in response to the inspections. Records of inspections must be maintained and be made readily available for inspection upon request.
 - (d) Employee Training - An employee training program must be developed to educate personnel responsible for implementing any component of the SWP3, or personnel otherwise responsible for storm water pollution prevention, with the provisions of the SWP3. The frequency of training must be documented in the SWP3, and at a minimum, must consist of one training prior to the initiation of operation of the concrete batch plant.
 - (e) Record Keeping and Internal Reporting Procedures - A description of spills and similar incidents, plus additional information that is obtained regarding the quality and quantity of storm water discharges, must be included in the SWP3. Inspection and maintenance activities must be documented and records of those inspection and maintenance activities must be incorporated in the SWP3.
 - (f) Management of Runoff - The SWP3 shall contain a narrative consideration for reducing the volume of runoff from concrete batch plants by diverting runoff or otherwise managing runoff, including use of infiltration, detention ponds, retention ponds, or reusing of runoff.
3. Comprehensive Compliance Evaluation – At least once per year, one or more qualified personnel (i.e., a person or persons with knowledge of this general permit, the concrete batch plant, and the SWP3 related to the concrete batch plant(s) for the site) shall conduct a compliance evaluation of the plant. The evaluation must include the following.
- (a) Visual examination of all areas draining storm water associated with regulated concrete batch plants for evidence of, or the potential for, pollutants entering the drainage system. These include but are not limited to: cleaning areas, material handling areas, above ground storage tanks, hoppers or silos, dust collection/containment systems, and truck wash down and equipment cleaning areas. Measures implemented to reduce pollutants in runoff (including structural controls and implementation of management practices) must be evaluated to determine if they are effective and if they are implemented in accordance with the terms of this permit

and with the permittee's SWP3. The operator shall conduct a visual inspection of equipment needed to implement the SWP3, such as spill response equipment.

- (b) Based on the results of the evaluation, the following must be revised as appropriate within two weeks of the evaluation: the description of potential pollutant sources identified in the SWP3 (as required in Part IV.B.1., "Description of Potential Pollutant Sources"); and pollution prevention measures and controls identified in the SWP3 (as required in Part IV.B.2., "Measures and Controls"). The revisions may include a schedule for implementing the necessary changes.
- (c) The permittee shall prepare and include in the SWP3 a report summarizing the scope of the evaluation, the personnel making the evaluation, the date(s) of the evaluation, major observations relating to the implementation of the SWP3, and actions taken in response to the findings of the evaluation. The report must identify any incidents of noncompliance. Where the report does not identify incidences of noncompliance, the report must contain a statement that the evaluation did not identify any incidence(s), and the report must be signed according to 30 TAC Section 305.128, relating to Signatories to Reports.
- (d) The Comprehensive Compliance Evaluation may substitute for one of the required inspections delineated in Part IV.B.2.(c) of this general permit.

Section C. Prohibition of Wastewater Discharges

Wastewater discharges associated with concrete production including wastewater disposal by land application are not authorized under this general permit. These wastewater discharges must be authorized under an alternative TCEQ water quality permit or otherwise disposed of in an authorized manner. Discharges of concrete truck washout at construction sites may be authorized if conducted in accordance with the requirements of Part V of this general permit.

Part V. Concrete Truck Wash Out Requirements

This general permit authorizes the wash out of concrete trucks at construction sites regulated under Sections II.E.1., 2., and 3. of this general permit, provided the following requirements are met. Authorization is limited to the land disposal of wash out water from concrete trucks that are associated with off-site production facilities. Wash out water associated with on-site concrete production facilities must be authorized under a separate TCEQ general permit or individual permit.

1. Direct discharge of concrete truck wash out water to surface water in the state, including discharge to storm sewers, is prohibited by this general permit.
2. Concrete truck wash out water shall be discharged to areas at the construction site where structural controls have been established to prevent direct discharge to surface waters, or to areas that have a minimal slope that allow infiltration and filtering of wash out water to prevent direct discharge to surface waters. Structural controls may consist of temporary berms, temporary shallow pits, temporary storage tanks with slow rate release, or other reasonable measures to prevent runoff from the construction site.
3. Wash out of concrete trucks during rainfall events shall be minimized. The direct discharge

- of concrete truck wash out water is prohibited at all times, and the operator shall insure that its BMPs are sufficient to prevent the discharge of concrete truck washout as the result of rain.
4. The discharge of wash out water shall not cause or contribute to groundwater contamination.
 5. If a SWP3 is required to be implemented, the SWP3 shall include concrete wash out areas on the associated map.

Part VI. Retention of Records

The permittee must retain the following records for a minimum period of three (3) years from the date that a NOT is submitted as required by Part II.E.3. For activities in which an NOT is not required, records shall be retained for a minimum period of three (3) years from the date that the operator terminates coverage under Section II.F.3. of this permit. Records include:

1. A copy of the SWP3;
2. All reports and actions required by this permit, including a copy of the construction site notice;
3. All data used to complete the NOI, if an NOI is required for coverage under this general permit; and
4. All records of submittal of forms submitted to the operator of any MS4 receiving the discharge and to the secondary operator of a large construction site, if applicable.

Part VII. Standard Permit Conditions

1. The permittee has a duty to comply with all permit conditions. Failure to comply with any permit condition is a violation of the permit and statutes under which it was issued, and is grounds for enforcement action, for terminating coverage under this general permit, or for requiring a discharger to apply for and obtain an individual TPDES permit.
2. Authorization under this general permit may be suspended or revoked for cause. Filing a notice of planned changes or anticipated non-compliance by the permittee does not stay any permit condition. The permittee must furnish to the executive director, upon request and within a reasonable time, any information necessary for the executive director to determine whether cause exists for revoking, suspending, or terminating authorization under this permit. Additionally, the permittee must provide to the executive director, upon request, copies of all records that the permittee is required to maintain as a condition of this general permit.
3. It is not a defense for a discharger in an enforcement action that it would have been necessary to halt or reduce the permitted activity to maintain compliance with the permit conditions.
4. Inspection and entry shall be allowed under Texas Water Code Chapters 26-28, Texas Health and Safety Code §§361.032-361.033 and 361.037, and 40 Code of Federal Regulations (CFR) §122.41(i). The statement in Texas Water Code §26.014 that commission entry of a facility shall occur according to an establishment's rules and regulations concerning safety, internal security, and

fire protection is not grounds for denial or restriction of entry to any part of the facility or site, but merely describes the commission's duty to observe appropriate rules and regulations during an inspection.

5. The discharger is subject to administrative, civil, and criminal penalties, as applicable, under Texas Water Code §§26.136, 26.212, and 26.213 for violations including but not limited to the following:
 - a. negligently or knowingly violating the federal Clean Water Act (CWA), §§301, 302, 306, 307, 308, 318, or 405, or any condition or limitation implementing any sections in a permit issued under CWA, §402, or any requirement imposed in a pretreatment program approved under CWA, §§402(a)(3) or 402(b)(8);
 - b. knowingly making any false statement, representation, or certification in any record or other document submitted or required to be maintained under a permit, including monitoring reports or reports of compliance or noncompliance.
6. All reports and other information requested by the executive director must be signed by the person and in the manner required by 30 TAC §305.128 (relating to Signatories to Reports).
7. Authorization under this general permit does not convey property or water rights of any sort and does not grant any exclusive privilege.


Part VIII. Fees

1. A fee of must be submitted along with the NOI:
 - a. \$325 if submitting a paper NOI, or
 - b. \$225 if submitting a NOI electronically.
2. Fees are due upon submission of the NOI. An NOI will not be declared administratively complete unless the associated fee has been paid in full.
3. No separate annual fees will be assessed. The Water Quality Annual fee has been incorporated into the NOI fees as described above.

Appendix A: Automatic Authorization
Periods of Low Erosion Potential by County – Eligible Date Ranges


Andrews: Nov. 15 - Apr. 30	Kerr: Dec. 15 - Feb. 14
Archer: Dec. 15 - Feb. 14	Kimble: Dec. 15 - Feb. 14
Armstrong: Nov. 15 - Apr. 30	King: Dec. 15 - Feb. 14
Bailey: Nov. 1 - Apr. 30, or Nov. 15 - May 14	Kinney: Dec. 15 - Feb. 14
Baylor: Dec. 15 - Feb. 14	Knox: Dec. 15 - Feb. 14
Borden: Nov. 15 - Apr. 30	Lamb: Nov. 1 - Apr. 14, or Nov. 15 - Apr. 30
Brewster: Nov. 15 - Apr. 30	Loving: Nov. 1 - Apr. 30, or Nov. 15 - May 14
Briscoe: Nov. 15 - Apr. 30	Lubbock: Nov. 15 - Apr. 30
Brown: Dec. 15 - Feb. 14	Lynn: Nov. 15 - Apr. 30
Callahan: Dec. 15 - Feb. 14	Martin: Nov. 15 - Apr. 30
Carson: Nov. 15 - Apr. 30	Mason: Dec. 15 - Feb. 14
Castro: Nov. 15 - Apr. 30	Maverick: Dec. 15 - Feb. 14
Childress: Dec. 15 - Feb. 14	McCulloch: Dec. 15 - Feb. 14
Cochran: Nov. 1 - Apr. 30, or Nov. 15 - May 14	Menard: Dec. 15 - Feb. 14
Coke: Dec. 15 - Feb. 14	Midland: Nov. 15 - Apr. 30
Coleman: Dec. 15 - Feb. 14	Mitchell: Nov. 15 - Apr. 30
Collingsworth: Jan. 1 - Mar. 30, or Dec. 1 - Feb. 28	Moore: Nov. 15 - Apr. 30
Concho: Dec. 15 - Feb. 14	Motley: Nov. 15 - Jan. 14, or Feb. 1 - Mar. 30
Cottle: Dec. 15 - Feb. 14	Nolan: Dec. 15 - Feb. 14
Crane: Nov. 15 - Apr. 30	Oldham: Nov. 15 - Apr. 30
Crockett: Nov. 15 - Jan. 14, or Feb. 1 - Mar. 30	Parmer: Nov. 1 - Apr. 14, or Nov. 15 - Apr. 30
Crosby: Nov. 15 - Apr. 30	Pecos: Nov. 15 - Apr. 30
Culberson: Nov. 1 - May 14	Potter: Nov. 15 - Apr. 30
Dallam: Nov. 1 - Apr. 14, or Nov. 15 - Apr. 30	Presidio: Nov. 1 - Apr. 30, or Nov. 15 - May 14
Dawson: Nov. 15 - Apr. 30	Randall: Nov. 15 - Apr. 30
Deaf Smith: Nov. 15 - Apr. 30	Reagan: Nov. 15 - Apr. 30
Dickens: Nov. 15 - Jan. 14, or Feb. 1 - Mar. 30	Real: Dec. 15 - Feb. 14
Dimmit: Dec. 15 - Feb. 14	Reeves: Nov. 1 - Apr. 30, or Nov. 15 - May 14
Donley: Jan. 1 - Mar. 30, or Dec. 1 - Feb. 28	Runnels: Dec. 15 - Feb. 14
Eastland: Dec. 15 - Feb. 14	Schleicher: Dec. 15 - Feb. 14
Ector: Nov. 15 - Apr. 30	Scurry: Nov. 15 - Apr. 30
Edwards: Dec. 15 - Feb. 14	Shackelford: Dec. 15 - Feb. 14
El Paso: Jan. 1 - Jul. 14, or May 15 - Jul. 31, or Jun. 1 - Aug. 14, or Jun. 15 - Sept. 14, or Jul. 1 - Oct. 14, or Jul. 15 - Oct. 31, or Aug. 1 - Apr. 30, or Aug. 15 - May 14, or Sept. 1 - May 30, or Oct. 1 - Jun. 14, or Nov. 1 - Jun. 30, or Nov. 15 - Jul. 14	Sherman: Nov. 15 - Apr. 30
Fisher: Dec. 15 - Feb. 14	Stephens: Dec. 15 - Feb. 14
Floyd: Nov. 15 - Apr. 30	Sterling: Nov. 15 - Apr. 30
Foard: Dec. 15 - Feb. 14	Stonewall: Dec. 15 - Feb. 14
Gaines: Nov. 15 - Apr. 30	Sutton: Dec. 15 - Feb. 14
Garza: Nov. 15 - Apr. 30	Swisher: Nov. 15 - Apr. 30
Glasscock: Nov. 15 - Apr. 30	Taylor: Dec. 15 - Feb. 14
Hale: Nov. 15 - Apr. 30	Terrell: Nov. 15 - Apr. 30
Hall: Feb. 1 - Mar. 30	Terry: Nov. 15 - Apr. 30
Hansford: Nov. 15 - Apr. 30	Throckmorton: Dec. 15 - Feb. 14
Hardeman: Dec. 15 - Feb. 14	Tom Green: Dec. 15 - Feb. 14
Hartley: Nov. 15 - Apr. 30	Upton: Nov. 15 - Apr. 30
Haskell: Dec. 15 - Feb. 14	Uvalde: Dec. 15 - Feb. 14
Hockley: Nov. 1 - Apr. 14, or Nov. 15 - Apr. 30	Val Verde: Nov. 15 - Jan. 14, or Feb. 1 - Mar. 30
Howard: Nov. 15 - Apr. 30	Ward: Nov. 1 - Apr. 14, or Nov. 15 - Apr. 30
Hudspeth: Nov. 1 - May 14	Wichita: Dec. 15 - Feb. 14
Hutchinson: Nov. 15 - Apr. 30	Wilbarger: Dec. 15 - Feb. 14
Irion: Dec. 15 - Feb. 14	Winkler: Nov. 1 - Apr. 30, or Nov. 15 - May 14
Jeff Davis: Nov. 1 - Apr. 30 or Nov. 15 - May 14	Yoakum: Nov. 1 - Apr. 30, or Nov. 15 - May 14
Jones: Dec. 15 - Feb. 14	Young: Dec. 15 - Feb. 14
Kent: Nov. 15 - Jan. 14 or Feb. 1 - Mar. 30	Wheeler: Jan. 1 - Mar. 30, or Dec. 1 - Feb. 28
	Zavala: Dec. 15 - Feb. 14

**Appendix B:
Erosivity Index (EI) Zones in Texas**

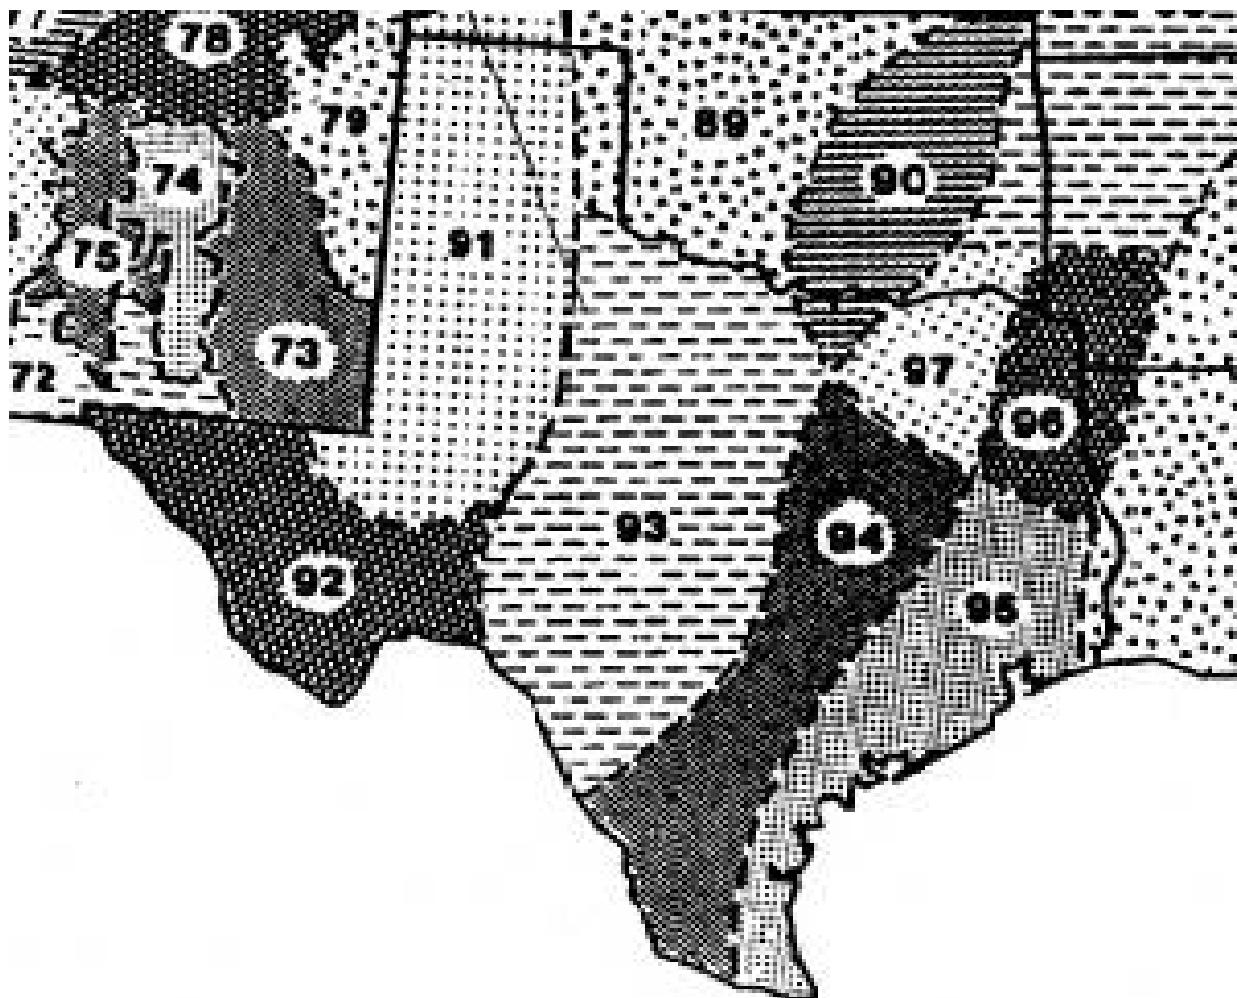

Adapted from Chapter 2 of USDA Agriculture Handbook 703: "Predicting Soil Erosion by Water: A Guide to Conservation Planning With the Revised Universal Soil Loss Equation (RUSLE)," U.S. Department of Agriculture, Agricultural Research Service

Appendix C: Isoerodent Map

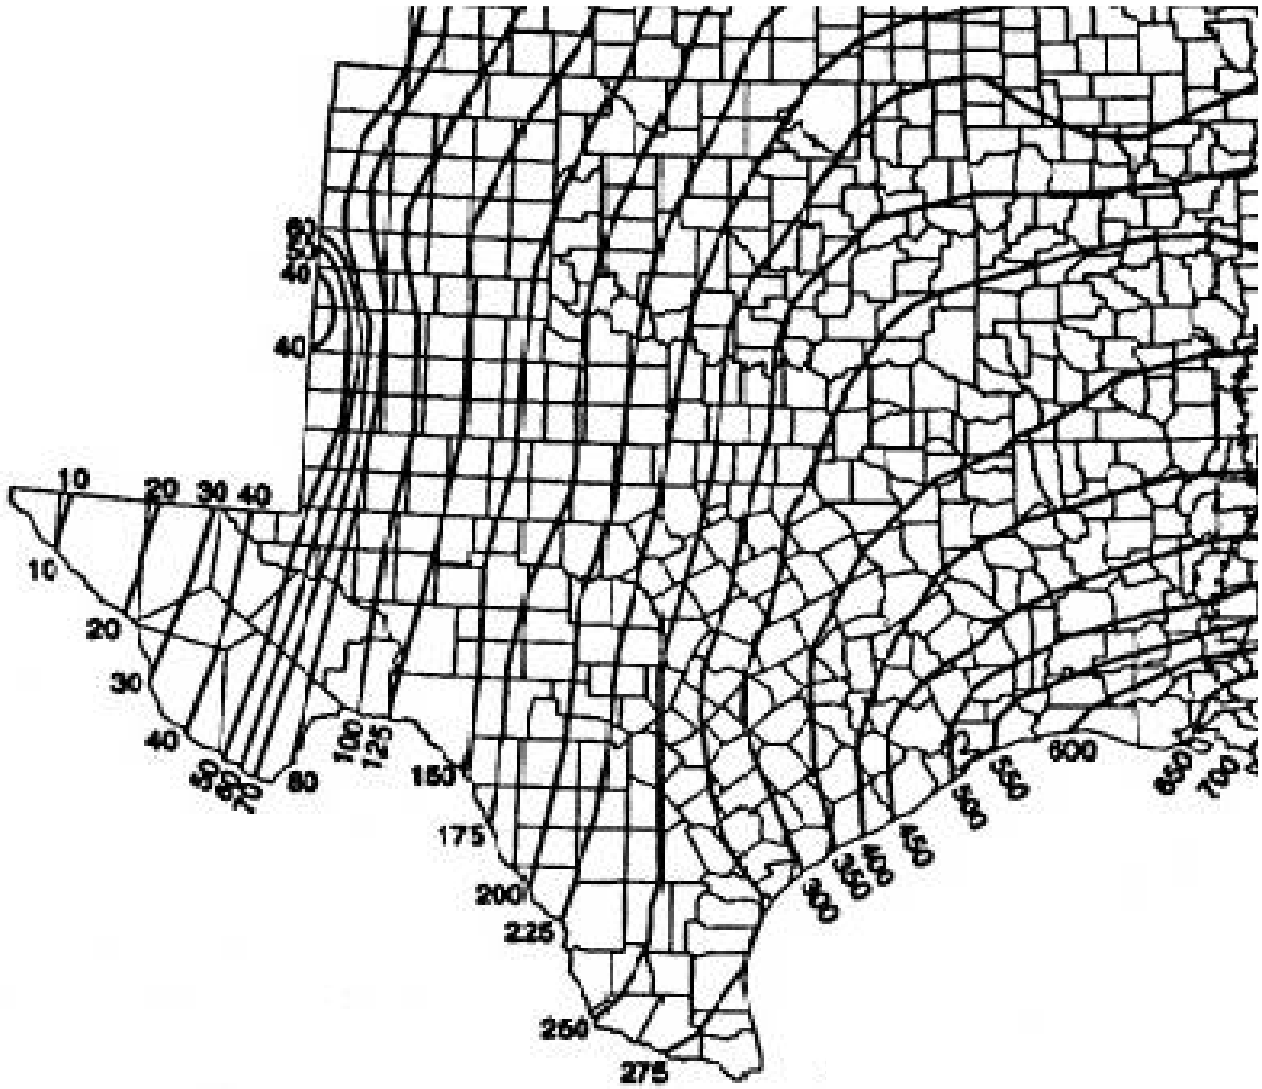

Adapted from Chapter 2 of USDA Agriculture Handbook 703: "Predicting Soil Erosion by Water: A Guide to Conservation Planning With the Revised Universal Soil Loss Equation (RUSLE)," U.S. Department of Agriculture, Agricultural Research Service

Appendix D: Erosivity Indices for EI Zones in Texas

Periods:

	1/1	1/15	2/1	2/15	3/1	3/15	4/1	4/15	5/1	5/15	6/1	6/15	7/1	7/15	8/1	8/15	9/1	9/15	10/1	10/15	11/1	11/15	12/1	12/15
89	0	0	1	1	2	3	4	7	12	18	27	38	48	55	62	69	76	83	90	94	97	98	99	100
90	0	1	2	3	4	6	8	13	21	29	37	46	54	60	65	69	74	81	87	92	95	97	98	99
91	0	0	0	0	1	1	1	2	6	16	29	39	46	53	60	67	74	81	88	95	99	99	100	100
92	0	0	0	0	1	1	1	2	6	16	29	39	46	53	60	67	74	81	88	95	99	99	100	100
93	0	1	1	2	3	4	6	8	13	25	40	49	56	62	67	72	76	80	85	91	97	98	99	99
94	0	1	2	4	6	8	10	15	21	29	38	47	53	57	61	65	70	76	83	88	91	94	96	98
95	0	1	3	5	7	9	11	14	18	27	35	41	46	51	57	62	68	73	79	84	89	93	96	98
96	0	2	4	6	9	12	17	23	30	37	43	49	54	58	62	66	70	74	78	82	86	90	94	97
97	0	1	3	5	7	10	14	20	28	37	48	56	61	64	68	72	77	81	86	89	92	95	98	99
106	0	3	6	9	13	17	21	27	33	38	44	49	55	61	67	71	75	78	81	84	86	90	94	97

* Each period begins on the date listed in the table above and lasts until the day before the following period. The final period begins on December 15 and ends on December 31.

Table adapted from Chapter 2 of USDA Agriculture Handbook 703: "Predicting Soil Erosion by Water: A Guide to Conservation Planning With the Revised Universal Soil Loss Equation (RUSLE)," U.S. Department of Agriculture, Agricultural Research Service

Attachment 1



**SMALL CONSTRUCTION SITE NOTICE:
LOW POTENTIAL FOR EROSION
FOR THE
Texas Commission on Environmental Quality (TCEQ)
Storm Water Program
TPDES GENERAL PERMIT TXR150000**

The following information is posted in compliance with **Part II.E.1.** of the TCEQ General Permit Number TXR150000 for discharges of storm water runoff from small construction sites automatically authorized based on low rainfall erosivity. Additional information regarding the TCEQ storm water permit program may be found on the internet at:
http://www.tceq.state.tx.us/nav/permits/wq_construction.html

Operator Name:	
Contact Name and Phone Number:	
Project Description: (Physical address or description of the site's location, estimated start date and projected end date, or date that disturbed soils will be stabilized)	

For Small Construction Sites Authorized Under Part II.E.1., the following certification must be completed:

I _____ (Typed or Printed Name Person Completing This Certification) certify under penalty of law that I have read and understand the eligibility requirements for claiming an automatic authorization based on low rainfall erosivity under Part II.E.1. of TPDES General Permit TXR150000 and agree to comply with the terms of this permit. Construction activities at this site shall occur within a time period listed in Appendix A of the TPDES general permit for this county, that period beginning on _____ and ending on _____. I understand that if construction activities continue past this period, all storm water runoff must be authorized under a separate provision of the general permit. A copy of this signed notice is supplied to the operator of the MS4 if discharges enter an MS4. I am aware there are significant penalties for providing false information or for conducting unauthorized discharges, including the possibility of fine and imprisonment for knowing violations.

Signature and Title _____ Date _____

Date Notice Removed
MS4 operator notified per Part II.F.3.

SMALL CONSTRUCTION SITE NOTICE

FOR THE Texas Commission on Environmental Quality (TCEQ) Storm Water Program **TPDES GENERAL PERMIT TXR150000**

The following information is posted in compliance with **Part II.E.2.** of the TCEQ General Permit Number TXR150000 for discharges of storm water runoff from small construction sites. Additional information regarding the TCEQ storm water permit program may be found on the internet at:
http://www.tceq.state.tx.us/nav/permits/wq_construction.html

Operator Name:	
Contact Name and Phone Number:	
Project Description: <i>Physical address or description of the site's location, estimated start date and projected end date, or date that disturbed soils will be stabilized</i>	
Location of Storm Water Pollution Prevention Plan:	

For Small Construction Activities Authorized Under Part II.E.2. (Obtaining Authorization to Discharge) the following certification must be completed:

I _____ (Typed or Printed Name Person Completing This Certification) certify under penalty of law that I have read and understand the eligibility requirements for claiming an authorization under Part II.D.2. of TPDES General Permit TXR150000 and agree to comply with the terms of this permit. A storm water pollution prevention plan has been developed and will be implemented prior to construction, according to permit requirements. A copy of this signed notice is supplied to the operator of the MS4 if discharges enter an MS4. I am aware there are significant penalties for providing false information or for conducting unauthorized discharges, including the possibility of fine and imprisonment for knowing violations.

Signature and Title _____ Date _____

_____ Date Notice Removed
_____ MS4 operator notified per Part II.F.3.

Attachment 3



LARGE CONSTRUCTION SITE NOTICE

FOR THE
Texas Commission on Environmental Quality (TCEQ)
Storm Water Program
TPDES GENERAL PERMIT TXR150000
“SECONDARY OPERATOR” NOTICE

This notice applies to secondary operators of construction sites operating under Part II.E.3. of the TPDES General Permit Number TXR150000 for discharges of storm water runoff from construction sites equal to or greater than five acres, including the larger common plan of development. The information on this notice is required in Part III.E.2. of the general permit. Additional information regarding the TCEQ storm water permit program may be found on the internet at: http://www.tceq.state.tx.us/nav/permits/sw_permits.html

Site-Specific TPDES Authorization Number:	
Operator Name:	
Contact Name and Phone Number:	
Project Description: <i>Physical address or description of the site's location, and estimated start date and projected end date, or date that disturbed soils will be stabilized.</i>	
Location of Storm Water Pollution Prevention Plan (SWP3):	

For Large Construction Activities Authorized Under Part II.E.3. (Obtaining Authorization to Discharge) the following certification must be completed:

I _____ (Typed or Printed Name Person Completing This Certification) certify under penalty of law that I have read and understand the eligibility requirements for claiming an authorization under Part II.E.2. of TPDES General Permit TXR150000 and agree to comply with the terms of this permit. A storm water pollution prevention plan has been developed and will be implemented prior to construction, according to permit requirements. A copy of this signed notice is supplied to the operator of the MS4 if discharges enter an MS4. I am aware there are significant penalties for providing false information or for conducting unauthorized discharges, including the possibility of fine and imprisonment for knowing violations.

Signature and Title _____ Date _____

_____ Date Notice Removed
 _____ MS4 operator notified per Part II.F.3.

Attachment 4



LARGE CONSTRUCTION SITE NOTICE

FOR THE
 Texas Commission on Environmental Quality (TCEQ)
 Storm Water Program
TPDES GENERAL PERMIT TXR150000

“PRIMARY OPERATOR” NOTICE

This notice applies to construction sites operating under Part II.E.3. of the TPDES General Permit Number TXR150000 for discharges of storm water runoff from construction sites equal to or greater than five acres, including the larger common plan of development. The information on this notice is required in Part III.E.2. of the general permit. This notice shall be posted along with a copy of the signed Notice of Intent (NOI), as applicable. Additional information regarding the TCEQ storm water permit program may be found on the internet at: http://www.tceq.state.tx.us/nav/permits/sw_permits.html

Site-Specific TPDES Authorization Number:	
Operator Name:	
Contact Name and Phone Number:	
Project Description: <i>Physical address or description of the site’s location, and estimated start date and projected end date, or date that disturbed soils will be stabilized.</i>	
Location of Storm Water Pollution Prevention Plan:	

APPENDIX B
CONSTRUCTION SITE NOTICE



SMALL CONSTRUCTION SITE NOTICE

FOR THE
Texas Commission on Environmental Quality (TCEQ)
Storm Water Program
TPDES GENERAL PERMIT TXR150000


The following information is posted in compliance with **Part II.E.2.** of the TCEQ General Permit Number TXR150000 for discharges of storm water runoff from small construction sites. Additional information regarding the TCEQ storm water permit program may be found on the internet at:

http://www.tceq.state.tx.us/nav/permits/wq_construction.html

Operator Name:	Klay Patteson (830) 624-8723 (USA Environment)
Contact Name and Phone Number:	Julie Burdey (512) 719-6062 (Parsons)
Project Description: <i>Physical address or description of the site's location, estimated start date and projected end date, or date that disturbed soils will be stabilized</i>	Camp Stanley Storage Activity (CSSA) 25800 Ralph Fair Road, Boerne, TX 78015 RMU-3 Excavation Construction Start Date: November 12, 2012 Construction End Date: May 31, 2013
Location of Storm Water Pollution Prevention Plan:	CSSA Environmental Office

For Small Construction Activities Authorized Under Part II.E.2. (Obtaining Authorization to Discharge) the following certification must be completed:

I Julie Burdey, P.G. (Typed or Printed Name Person Completing This Certification) certify under penalty of law that I have read and understand the eligibility requirements for claiming an authorization under Part II.E.2. of TPDES General Permit TXR150000 and agree to comply with the terms of this permit. A storm water pollution prevention plan has been developed and will be implemented prior to construction, according to permit requirements. A copy of this signed notice is supplied to the operator of the MS4 if discharges enter an MS4. I am aware there are significant penalties for providing false information or for conducting unauthorized discharges, including the possibility of fine and imprisonment for knowing violations.

Signature and Title  Date 11/8/2012

MS4 operator notified per Part II.F.3. *Date Notice Removed*

**APPENDIX C
INSPECTION FORM
(10 COPIES)**

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____

**CSSA RMU-3 Investigation
Storm Water Pollution Prevention Plan
Inspection and Maintenance Report Form**

Inspections must be conducted at least once every fourteen (14) calendar days and within twenty four (24) hours of the end of a storm event of 0.5 inches or greater.

Inspector: _____ Date: _____

Inspector's Title/Qualifications: _____

Days since last rainfall: _____ Amount of last rainfall: _____ inches

Dates when major grading activities occurred: _____ (once per occurrence)

Comment: _____

Dates when construction activities temporarily or permanently cease on a portion of the site: _____ (once per occurrence)

Comment: _____

Dates when stabilization measures were initiated: _____ (once per occurrence)

Comment: _____

Are grassland buffer zones and silt fences capturing sediment during rain events and performing properly: _____

Comments/ Corrective Actions: _____

I certify that the construction site is in conformance with the RMU-3 Storm Water Pollution Prevention Plan.

Inspectors Signature: _____

Date: _____
